

## Section 5 - Facilities


### Sub-Section



## SCHOOL SPOTLIGHTS

# UNDERSTANDING THE SIX-PHASE PROCESS

To ensure projects are completed with the utmost efficiency and integrity, each project typically goes through a six-phase process.

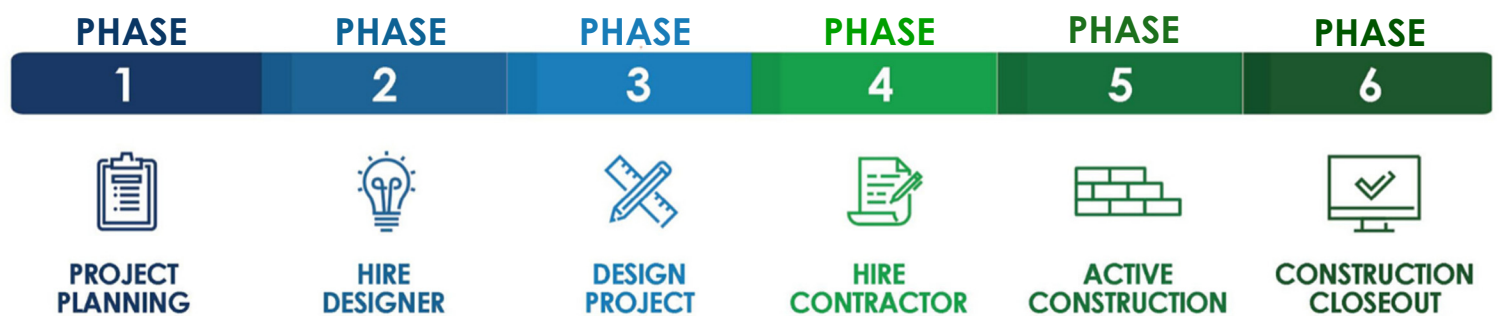

## PHASE 1



### PROJECT PLANNING

The Planning phase (Phase 1) is the initiation phase of a project. During this phase, the scope of work is assembled, and a delivery method is chosen based on the complexity and size of the scope. The selected delivery method can be a traditional Design/Bid/Build method, a Construction Management at Risk method, or the use of task order contracts that are currently in place between the District, Professional Service Firms, and Contractors.

## PHASE 2



### HIRE DESIGNER

The Hire Designer phase (Phase 2) represents the various steps involved in hiring a professional Design team. It begins with the advertising for Requests for Qualification (RFQ) from design firms, then going through the selection process with the Qualification Evaluation Selection Committee (QSEC) and ends with the issuance of an Authorization to Proceed (ATP) with design work.

# UNDERSTANDING THE SIX-PHASE PROCESS

## PHASE

3



**DESIGN  
PROJECT**

## DESIGN

The Design phase (Phase 3) starts after the ATP has been issued. The selected design firm begins by holding a kickoff meeting with the Owner Representative and school administration in order to perform a more detailed scope validation, then moves into the development of drawings and plans needed to hire a contractor and implement the work.

### THE DESIGN PROCESS EXPLAINED

#### 0-20%

Defining and validating general scope of the project

#### 20-50%

Beginning to develop construction documents

#### 50-70%

Incorporating details and specifications into construction documents

#### 70-90%

Construction documents are nearing completion for permitting

#### 90-95%

Construction documents undergo internal review process

#### 95-100%

Drawings are reviewed by the Building Department for permitting.

Once a Letter of Recommendation (LOR) is received, the phase is complete.

# UNDERSTANDING THE SIX-PHASE PROCESS

## PHASE

4



HIRE  
CONTRACTOR

## HIRE CONTRACTOR

The Hire Contractor phase (Phase 4) begins by hiring a contractor or vendor and ends with the issuing of a Notice To Proceed (NTP). This process can be completed in various forms and delivery methods, including Invitations To Bid (ITB), Construction Management at Risk (CMAR), or leveraging approved continuing services contracts.

### THE HIRE CONTRACTOR PROCESS EXPLAINED

#### 0-30%

Advertisement of the Invitation to Bid / CM assembling design documents

#### 30-50%

Bids received and reviewed / CM collecting sub-contractor bids

#### 50-80%

Bid negotiations held / CM submits GMP proposal

#### 80-100%

Award and execution of the contracts / execution of contract amendment

## PHASE

5



ACTIVE  
CONSTRUCTION

## CONSTRUCTION

The Construction phase (Phase 5) begins after the NTP that authorizes the contractor/vendor to start working has been issued. The process includes all aspects required to execute approved scope of work through substantial completion.



# UNDERSTANDING THE SIX-PHASE PROCESS

## PHASE

6



**CONSTRUCTION  
CLOSEOUT**

## CONSTRUCTION CLOSEOUT

The Construction Closeout phase takes place between substantial and final completion, which includes verification that the scope is completed according to approved specifications, final submittals of documents, and in closing out the vendor contract.

There are multiple steps within the Construction Closeout phase. Included below is a breakdown of these steps.

### THE CONSTRUCTION CLOSEOUT PROCESS EXPLAINED

#### 0-80%

##### **Substantial Completion**

Obtained with the certificate of occupancy, following close-out of construction

#### 80-100%

##### **Final Completion**

Accomplished when all punch-list items have been reviewed by the designer and approved by the inspector


#### 100%

##### **Board Approval**

The SBBC approves Final Change Order, Final Acceptance & Final Release of Retainage. This step represents the official completion of the project.

## WHAT'S NEW IN THE SCHOOL SPOTLIGHT

Additional changes have been made to address schedule and phase concerns. Once a project has completed construction and reached construction closeout, it will no longer receive a schedule flag while they are going through the punch list and closeout process. Before reaching the closeout phase, the school is issued a certificate of occupancy and the upgrades are in use.



**SCHOOL SPOTLIGHT**  
 QUARTER ENDING MARCH 31, 2020



**Long Middle School**  
 6831 SW 26 STREET, MIRAMAR 33023

Location Num	0531
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$6,557,935
Total Facilities Budget	\$6,184,935

\*NOTE This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBOC in September 2019. This budget includes Technology Improvements and Musical Instruments Replacements which are not included in this section of the report.  
 - All dates are based on calendar year. SMART funded projects are included. Only  
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

**PRIMARY PROJECTS CURRENT STATUS: Complete**

Primary Renovation: Substantial Completion has been reached. Project closeout is in progress with minor HVAC improvements needed to closeout the project.

School Choice Enhancements: COMPLETED 08/2018 - Voting completed 5/5/17; (75) student laptops and safety cones delivered 07/2017. (13) document cameras, stage curtains delivered 08/2017. Cafeteria sound system delivered and installed 12/2017. Picnic tables and cafeteria blinds delivered and installed 01/2018. Office furniture delivered 07/2018. Permit for the marquee issued 2/2/2018; Marquee installed 07/2018 and electrical tie-in completed 08/2018.

**SMART Facilities Update By Project**

**1**  
**PLANNING**  
Develop & Validate Project Scope

**2**  
**HIRE DESIGN TEAM**  
Advertise and Hire Design Team

**3**  
**DESIGN**  
Prepare Plan Drawings to release to contractor/vendor

**4**  
**HIRE CONTRACTOR**  
Bid and Hire Contractor to Implement Renovations

**5**  
**CONSTRUCTION**  
Contractor Implements Renovations

**6**  
**CONSTRUCTION CLOSEOUT**  
Final Inspection for Quality Assurance

**Primary Renovation**

Phase: 55% Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2016	Q2 2016	Q4 2016	Q3 2017	Q1 2018	Q1 2019
New Planned	Q1 2016	Q2 2016	Q4 2016	Q3 2017	Q4 2018	Q1 2020
Actual/Forecast	3/9/2016	5/17/2016	12/13/2016	6/15/2018	11/30/2018	11/20/2019 4/30/2020

**SCOPE:**

Additional Funding - Board Approved 11/07/18 (JJ-1)

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

HVAC Improvements

**BUDGET:**

\$2,286,935

\$855,000

\$2,943,000

**FLAG:**

**COMMENTS:**

**School Choice Enhancements\***

Phase: 100% Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q2 2017	Q2 2018
Actual	11/2015	05/2017	08/2018

**SCOPE:**

School Choice Enhancement

**BUDGET:**


\$100,000

**FLAG:**

**COMMENTS:**

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.

**CBRE | HEERY**  
**ATKINS**



### Construction Closeout

Projects in Construction Closeout will no longer receive a schedule flag.

**SAFETY  
MUSIC & ART  
ATHLETICS  
RENOVATION  
TECHNOLOGY**

SMART INVESTMENTS  
LEAD TO SMART STUDENTS.

Page 194 -- FY20 Q3



## Annabel C. Perry Pre K - 8

(f.k.a. Annabel C. Perry Elementary)

6850 SW 34 STREET, MIRAMAR 33023

Location Num	1631
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$5,478,037
Total Facilities Budget	\$5,115,037

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Construction


Primary Renovation: Construction in progress. HVAC and fire alarm work is complete. A new roofing sub-contractor has been brought on. Final steps for roofing completion are in progress.

School Choice Enhancements: COMPLETED 05/2018 - Voting completed 5/25/2016. Front office renovation completed 8/2016; (45) student laptops and a golf cart delivered 09/2016; Athletics equipment delivered 10/2016. Outdoor furniture delivered 11/2016.

Digital marquee installed and operational 11/2017. Floor mats delivered 11/2017. Front door wrap delivered and installed 12/2017.

Minifridge and presentation cabinets delivered 03/2018. Chain link fence art work delivered 05/2018.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **98% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2016	Q2 2016	Q4 2016	Q4 2017	Q1 2018	Q1 2019
New Planned	Q1 2016	Q2 2016	Q4 2016	Q4 2017	Q1 2018	Q3 2019
Actual/Forecast	3/9/2016	5/17/2016	12/14/2016	2/13/2018	10/16/2018	4/29/2020

#### SCOPE:

Additional Funding - Board Approved 05/22/18 (JJ-2)	\$1,950,037
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$967,000
Electrical Improvements	\$294,000
Fire Alarm	\$293,000
Fire Sprinklers	\$18,000
HVAC Improvements	\$1,170,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays occurred due to Fire Alarm Specification Changes and Roofing Contractor Issues with permitting. Remedy: Fire alarm delays near completion, all new devices are installed and tested, inspections are slated for early Q2. Roofing work is nearing completion on Building 1, which was held up due to some impacts from existing conditions that had an un-anticipated affect on completion.

## Annabel C. Perry Pre K - 8

(f.k.a. Annabel C. Perry Elementary)

### SMART Facilities Update by Project Cont.

#### Media Center

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2017	Q2 2017	Q1 2018	Q2 2018	Q1 2019	Q4 2019
New Planned	Q1 2017	Q2 2017	Q1 2018	Q2 2019	Q4 2019	Q2 2021
Actual/Forecast	3/7/2017	5/11/2017	8/9/2017	1/2/2019	6/6/2019	8/15/2019
Actual/Forecast	11/20/2019					
SCOPE:	BUDGET:		FLAG:			
Media Center improvements	\$323,000		COMMENTS:			

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design		PH:2 Implement		PH:3 Complete	
	Planned	Q1 2015	Q2 2016		Q1 2018	Q1 2018
	Actual	11/2015	05/2016		05/2018	05/2018
SCOPE:		BUDGET:		FLAG:		
School Choice Enhancement		\$100,000		COMMENTS:		

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Apollo Middle School

6800 ARTHUR STREET, HOLLYWOOD 33024

Location Num	1791
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$7,433,000
Total Facilities Budget	\$7,085,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. Design firm currently addressing Building Department comments prior to submitting the second time for permit application.

School Choice Enhancements: Voting completed 5/28/2019. ID maker machine delivered 10/2019. Cork Strips (29), and printer delivered 11/2019. iPhone strike completed 12/2019. (10) chairs delivered 02/2020. Logo Rugs delivered 02/2020. Signage Wayfinding on order. Digital Marquee in design.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **96% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2017	Q1 2018	Q4 2018	Q2 2019	Q4 2019	Q4 2020
New Planned	Q4 2017	Q1 2018	Q4 2018	Q4 2019	Q3 2020	Q1 2022
Actual/Forecast	9/1/2017	11/13/2017	5/2/2018	Q4 2020		

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,633,000
Fire Sprinklers	\$50,000
HVAC Improvements	\$4,570,000
Media Center improvements	\$555,000
Safety / Security Upgrade	\$107,000

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred during the design phase. The design firm has been delayed in submitting the construction documents for permit review. Remedy: The design has been submitted for permit review, and is currently being revised in order to resubmit.

#### Track

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	6/8/2016	7/8/2016

SCOPE:	BUDGET:
Track Resurfacing	\$70,000

**FLAG:**

#### COMMENTS:

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Apollo Middle School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **22% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q4 2018	Q2 2019	TBD	TBD
Actual	11/2018	05/2019		
<b>SCOPE:</b>	<b>BUDGET:</b>		<b>FLAG:</b>	
School Choice Enhancement	\$100,000		<b>COMMENTS:</b> Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Atlantic Technical College & Technical High School

4700 COCONUT CREEK PARKWAY, COCONUT CREEK 33063

Location Num	2221
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$10,340,400
Total Facilities Budget	\$9,052,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in review. Design firm preparing to submit for permit review.

School Choice Enhancements: COMPLETED 06/2017- Voting completed prior to October 2015 - Furniture/renovation for the media center; installation completed 06/2017.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **94% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2015	Q4 2015	Q3 2016	Q2 2018	Q3 2018	Q4 2019
New Planned	Q4 2015	Q4 2015	Q3 2016	Q4 2019	Q2 2020	Q3 2021
Actual/Forecast	10/29/2015	12/8/2015	9/23/2016	Q3 2020		

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$2,710,000
Fire Sprinklers	\$1,482,000
IAQ Repairs - HVAC	\$4,642,000
Media Center improvements	\$88,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred during the design phase. The design firm has not submitted design documents per the professional service agreement. Remedy: The owner will be enforcing terms of the contract for delays.

#### Media Center Improvements

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	N/A	11/1/2016

#### SCOPE:

Media Center improvements - Carpet and Paint	\$30,000
--	----------

#### BUDGET:

**FLAG:**

#### COMMENTS:

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Atlantic Technical College & Technical High School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **100% Complete**

<b>SCHEDULE:</b>	<b>PH:1 Planning/Design</b>		<b>PH:2 Implement</b>	<b>PH:3 Complete</b>
Planned	Q1 2016	N/A	Q2 2017	Q2 2017
Actual	01/2016	N/A	06/2017	06/2017
<b>SCOPE:</b>	<b>BUDGET:</b>		<b>FLAG:</b>	
School Choice Enhancement	\$100,000		<b>COMMENTS:</b>	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Atlantic Technical, Arthur Ashe, Jr Campus

1701 NW 23 AVENUE, FORT LAUDERDALE 33311

Location Num	4702
Board District	5
Board Member	Dr. Rosalind Osgood
ADEFP Budget*	\$3,326,449
Total Facilities Budget	\$3,178,449

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

## PRIMARY PROJECTS CURRENT STATUS: Construction

Primary Renovation: Construction in progress. Building 1 and 2 roofing is complete. Coping and lightning protection is being installed.

School Choice Enhancements: COMPLETED 12/2016- Voting completed prior to October 2015 - Renovation/furniture for the Media Center. Installation completed 12/2016.

## SMART Facilities Update By Project



### Primary Renovation

Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2017	Q2 2017	Q2 2017	Q4 2017	Q3 2018	Q3 2019
New Planned	Q1 2017	Q2 2017	Q2 2017	Q4 2017	Q1 2019	Q1 2020
Actual/Forecast	10/29/2016	3/27/2017	4/27/2017	9/21/2018	2/15/2019	6/24/2020

#### SCOPE:

Additional Funding - Board Approved 01/15/19 (JJ-2)

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

Fire Alarm

#### BUDGET:

\$1,836,449

\$1,200,000

\$42,000

#### FLAG: S - Project Delayed

#### COMMENTS:

Original contractual date of substantial completion is 8/20/2019. Reason: Delays occurred during construction related to the roofing sub-permit. It took an estimated additional 4 months in order to receive an approved roofing sub-permit which was not accounted for in the original construction schedule. Additional delays were experienced beginning the roof work after the sub-permit was received. Remedy: The sub-permit has been received, the roof repairs are complete, and the construction is estimated to be completed in Q2 2020.

FLAG KEY: S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Atlantic Technical, Arthur Ashe, Jr Campus

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **100% Complete**

SCHEDULE:				
	PH:1 Planning/Design		PH:2 Implement	
	PH:3 Complete			
Planned	Q1 2015	N/A	Q3 2016	Q3 2016
Actual	11/2015	N/A	12/2016	12/2016
SCOPE:		BUDGET:	FLAG:	
School Choice Enhancement		\$100,000	COMMENTS:	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Atlantic West Elementary School

301 NW 69 TERRACE, MARGATE 33063

Location Num	2511
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$3,070,197
Total Facilities Budget	\$2,717,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. Design firm currently addressing Building Department comments prior to submitting the second time for permit application. Negotiations with the design firm are taking place related to additional funding for increase scope.

School Choice Enhancements: Voting completed 10/20/17 - Janitorial Equipment, and folding chairs delivered 12/2017. Marquee permit issued 2/7/2018; installed 05/2018. Front Office Renovation furniture delivered 04/2018. Shade Structure in PE court permitted 12/2018. Pre-construction meeting held 2/12/2019; construction scheduled 7/1/2019.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2016	Q2 2016	Q1 2017	Q4 2017	Q2 2018	Q1 2019
New Planned	Q2 2016	Q2 2016	Q1 2017	Q2 2019	Q4 2019	Q1 2021
Actual/Forecast	4/22/2016	6/21/2016	1/30/2017	Q3 2020		

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,048,000
Fire Sprinklers	\$619,000
HVAC Improvements	\$723,000
Media Center improvements	\$227,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred in the design phase. The design firm has taken an above average amount of time to complete the 100% submittal. Remedy: The owner will be enforcing terms of the contract for delays.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Atlantic West Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **73% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q1 2016	Q4 2017	TBD	TBD
Actual	01/2016	10/2017		
<b>SCOPE:</b>				
School Choice Enhancement				
<b>BUDGET:</b>				
	\$100,000			
<b>FLAG:</b>	<b>S - Project Delayed</b>			
<b>COMMENTS:</b>	Shade is under construction.			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Attucks Middle School

3500 N 22 AVENUE, HOLLYWOOD 33020

Location Num	0343
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$4,361,903
Total Facilities Budget	\$4,058,903

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation - Phase 1: 100% Construction Documents in the permitting process. Design firm currently addressing Building Department comments prior to submitting the sixth time for permit application.

Primary Renovation - Roofing: Letter of Recommendation to permit has been received on the roofing and media center scope of work. Media Center and Roofing project has been split to achieve better pricing for construction. Project requires repermitting of the design.

School Choice Enhancements: COMPLETED 2/2017- Voting completed 1/21/16 - Front office renovation, murals, facilities equipment, technology, lab remodeling, media center upgrade, LCD projectors and an interior audio system. All items installed and delivered 2/27/17.

### SMART Facilities Update By Project



#### Primary Renovation - Phase 1

Phase: **98% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2016	Q3 2016	Q2 2017	Q4 2017	Q3 2018	Q2 2019
New Planned	Q2 2016	Q3 2016	Q2 2017	Q2 2019	Q4 2019	Q1 2021
Actual/Forecast	5/17/2016	7/26/2016	5/2/2017	Q2 2020		

#### SCOPE:

Electrical Improvements	\$624,000
HVAC Improvements	\$454,000
Provide Fire Sprinkler Protection Install New Fire Alarm	\$1,962,778

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred in the design process related to permitting and minor delays during design. Multiple revisions have been required by the design firm in order to achieve a permit, with minor edits required to receive permit. Pending submission of the sixth submission. Remedy: The owner will be enforcing terms of the

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Attucks Middle School

### SMART Facilities Update by Project Cont.

#### Primary Renovation - Roofing

Phase: **5% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2017	Q1 2017	Q2 2017	Q3 2017	Q4 2017	Q2 2019
New Planned	Q1 2017	Q1 2017	Q2 2017	Q1 2019	Q2 2019	Q2 2020
Actual/Forecast	2/9/2017	2/9/2017	4/20/2017	2/13/2019	Q3 2020	

<b>SCOPE:</b> Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	<b>BUDGET:</b> \$498,125	<b>FLAG: S - Project Delayed</b>
<b>COMMENTS:</b> Reason: Delays occurred during bid and award due to contractor pricing. Remedy: Negotiations with the CSMP Contractor were held and the project was split into two projects to achieve better pricing. Pending permit review prior to executing proposal and Notice to Proceed from contractor.		

#### Primary Renovation - Media Center

Phase: **5% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
New Planned	Q1 2017	Q1 2017	Q2 2017	Q1 2019	Q2 2019	Q2 2020
Actual/Forecast	2/9/2017	2/9/2017	4/20/2017	2/13/2019	Q3 2020	

<b>SCOPE:</b> Media Center improvements	<b>BUDGET:</b> \$420,000	<b>FLAG: S - Project Delayed</b>
<b>COMMENTS:</b> Reason: Delays occurred during bid and award due to contractor pricing. Remedy: Negotiations with the CSMP Contractor were held and the project was split into two projects to achieve better pricing. Pending permit review prior to executing proposal and Notice to Proceed from contractor.		

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q1 2016	Q1 2017
Actual	01/2015	01/2016	02/2017

<b>SCOPE:</b> School Choice Enhancement	<b>BUDGET:</b> \$100,000	<b>FLAG:</b>
<b>COMMENTS:</b>		

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Bair Middle School

9100 NW 21 MANOR, SUNRISE 33322

Location Num	2611
Board District	5
Board Member	Dr. Rosalind Osgood
ADEFP Budget*	\$1,998,000
Total Facilities Budget	\$1,617,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

## PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Bid advertisement is scheduled for April 2020.

School Choice Enhancements: COMPLETED 10/2018 - Voting authorized 5/15/18 - Voting completed 6/1/2018 - Projector and Portable Sound System delivered 08/2018. Cafeteria Sound system installed 09/2018. Indoor Office Furniture delivered 10/2018. Laptops (22) and (1) earthcart delivered 10/2018.

## SMART Facilities Update By Project



### Primary Renovation

Phase: 5% Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2017	Q4 2017	Q3 2018	Q1 2019	Q3 2019	Q2 2020
New Planned	Q3 2017	Q4 2017	Q3 2018	Q3 2019	Q1 2020	Q1 2021
Actual/Forecast	5/1/2017	7/20/2017	3/14/2018	9/5/2019	Q4 2020	

### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$380,000
Fire Alarm	\$462,000
HVAC Improvements	\$103,000
Media Center improvements	\$495,000
Safety / Security Upgrade	\$77,000

### BUDGET:

FLAG: S - Project Delayed

### COMMENTS:

Funding Year 1 thru 3 projects are to take priority for advertisement of bid. The project is funded under Year 4 and will be advertised after the funding Year 1 thru 3 projects that are prepared for advertisement.

FLAG KEY: S=Schedule B= Budget

S-Project Delayed=Schedule: Project has missed the planned milestone date for progressing to the next phase in the process.

S-Delay Possible=Schedule: Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

B=Budget: reflects a need for board approved increase in funding based on bid and/or change order results.



## Bair Middle School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2017	Q2 2018	Q1 2019
Actual	11/2017	06/2018	10/2018
SCOPE:	BUDGET:		
School Choice Enhancement	\$100,000		
		FLAG:	
		COMMENTS:	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Banyan Elementary School

8800 NW 50 STREET, SUNRISE 33351

Location Num	2001
Board District	5
Board Member	Dr. Rosalind Osgood
ADEFP Budget*	\$2,633,224
Total Facilities Budget	\$2,316,224

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. Roofing submittals are in progress. Media Center and bathroom improvements are complete.

School Choice Enhancements: Voting completed May 2016. Murals complete 02/2017. Marquee PO canceled for Robson Corporation; District is no longer using this vendor due to lack of performance. PO placed with a new vendor 05/2019. Playground upgrades permit received; construction completed 12/2018. PO request issued for new marquee vendor 04/2019; marquee permitted 10/17/2019; pre-construction meeting scheduled for 10/30/2019. Structural construction completed 12/2019; electrical tie-in completed 01/2020.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **50% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2016	Q4 2016	Q2 2017	Q4 2017	Q2 2018	Q2 2019
New Planned	Q4 2016	Q4 2016	Q2 2017	Q4 2017	Q1 2019	Q3 2019
Actual/Forecast	10/20/2016	10/20/2016	3/28/2017	8/13/2018	3/1/2019	6/24/2020

#### SCOPE:

Additional Funding - Board Approved 01/15/19 (JJ-4)	\$962,979
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$917,000
HVAC Improvements	\$128,000
Media Center improvements	\$198,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Original contractual date of substantial completion is 9/3/2019. Reason: Delays occurred during construction related to the roofing sub-permit. The project continues to be delayed until the roofing sub-permit is received. Remedy: The construction is estimated to be completed in Q2 2020 pending receipt of the sub-permit.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Banyan Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **74% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q1 2015	Q2 2016	Q2 2018	Q2 2018
Actual	11/2015	05/2016		
<b>SCOPE:</b>	<div> <div>Additional Funding - Board Approved 04/23/19 (JJ-12)</div> <div>School Choice Enhancement</div> </div>			
<b>BUDGET:</b>	<div> <div>\$10,245</div> <div>\$100,000</div> </div>			
<b>FLAG:</b>	<b>S - Project Delayed</b>			
<b>COMMENTS:</b>	New Marquee vendor hired to replace previous vendor. Previous vendor replaced due to poor performance.			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Bayview Elementary School

1175 MIDDLE RIVER DRIVE, FORT LAUDERDALE 33304

Location Num	0641
Board District	3
Board Member	Heather P. Brinkworth
ADEFP Budget*	\$3,019,739
Total Facilities Budget	\$2,788,739

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Construction

Primary Renovation: Construction in progress. Project is nearing substantial completion. Pending contractor submitting schedule showing delays impacted, and completion of final roofing work to reach substantial completion.

School Choice Enhancements: COMPLETED 03/2020 - Voting authorized 1/24/18. Voting completed 2/15/18. Cafeteria sound system installed 04/2018. Printers, Poster Maker and Parking stations delivered 05/2018. Furniture (Tables, Chairs for 3rd, 4th and 5th Grade) delivered 07/2018

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **97% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2016	Q2 2017	Q2 2017	Q4 2017	Q3 2018	Q3 2019
New Planned	Q3 2016	Q2 2017	Q2 2017	Q4 2017	Q3 2018	Q3 2019
Actual/Forecast	9/14/2016	9/14/2016	4/25/2017	3/21/2018	10/19/2018	4/30/2020

#### SCOPE:

Additional Funding - Board Approved 06/26/18 (JJ-6)

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

HVAC Improvements

#### BUDGET:

\$946,739

\$836,000

\$645,565

#### FLAG: S - Project Delayed

#### COMMENTS:

Original contractual date of substantial completion is 4/23/2019. Reason: Delays have occurred during construction related to multiple inspections and follow-up work needed to pass the inspections. Remedy: The project is pending final roof repairs and inspections. Update: December rains prevented substantial completion by the end of 2019 with majority of the final work being roof repairs. Roofing work continues to be delayed due to contractor not able to pass inspections. Substantial completion is now scheduled for early April 2020.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Bayview Elementary School

### SMART Facilities Update by Project Cont.

#### HVAC Improvements

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout	
Planned	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	N/A	N/A	3/21/2018

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
HVAC Improvements - Chiller Replacement	\$260,435	<b>COMMENTS:</b>

#### School Choice Enhancements\*

Phase: **98% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete	
Planned	Q4 2016	Q1 2018	Q1 2020	Q1 2020
Actual	12/2016	02/2018	03/2020	03/2020

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
School Choice Enhancement	\$100,000	<b>COMMENTS:</b>

All items approved by voting process have been purchased, delivered and installed. (1) Lenovo computer is on order with remaining contingency portion of the SCEP funding.

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Beachside Montessori Village

2230 LINCOLN STREET, HOLLYWOOD 33020

Location Num	2041
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$441,000
Total Facilities Budget	\$100,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.


- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


### PRIMARY PROJECTS CURRENT STATUS: N/A

School Choice Enhancements: COMPLETED 01/2018 - Voting completed 2/28/16. Music equipment, athletic equipment, math and science equipment, and the portable sound system delivered 12/2016. Cafeteria audio system delivered and installed 08/2017. Microscopes delivered 12/2017. Cabinets and (29) laptops delivered 01/2018.

### SMART Facilities Update By Project



#### School Choice Enhancements\*

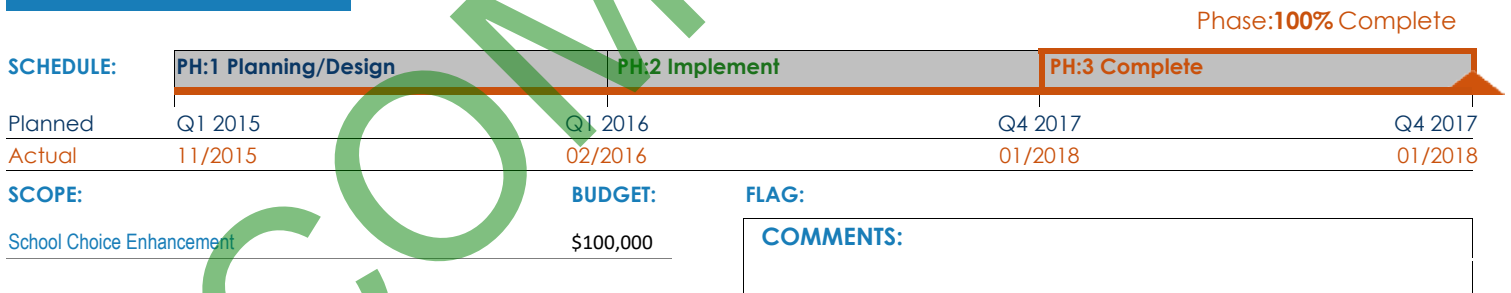

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.



## Bennett Elementary School

1755 NE 14 STREET, FORT LAUDERDALE 33304

Location Num	0201
Board District	3
Board Member	Heather P. Brinkworth
ADEFP Budget*	\$2,119,000
Total Facilities Budget	\$1,914,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 90% Construction Documents in progress. District decisions are required for the demolition or renovation of multiple buildings. Discussions pending Board workshop in January 2020.

School Choice Enhancements: Kick-off meeting held 2/15/2019. Voting authorized 4/25/2019. Golf cart delivered 06/2019. Office and classroom furniture, furniture for reception area and AP office, desk with reception top, cube tables, cabinets, (180) open front student desk, (180) chairs, (7) tables, (24) stools delivered 08/2019. New 4'x8' digital marquee on order.

### SMART Facilities Update By Project



#### Primary Renovation

 Phase: **88% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q1 2019	Q3 2019	Q2 2020	Q1 2021
New Planned	Q1 2018	Q2 2018	Q1 2019	Q1 2020	Q2 2020	Q2 2021
Actual/Forecast	8/1/2017	10/6/2017	5/3/2018	Q4 2020		

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,270,000
Fire Alarm	\$319,000
HVAC Improvements	\$88,000
Media Center improvements	\$137,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

The project included the demolition or renovation of multiple campus buildings. The project is pending a presentation to the Board on demolition or renovation prior to completing the design. Once the decisions are made the project will progress to 100% Construction Documents and then the permitting process.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Bennett Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **54% Complete**

SCHEDULE:		PH:1 Planning/Design		PH:2 Implement		PH:3 Complete	
Planned	Q4 2018	Q1 2019	TBD	TBD			
Actual	11/2018	04/2019					
SCOPE:		BUDGET:		FLAG:			
School Choice Enhancement		\$100,000		<div>COMMENTS:</div> <p>Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.</p>			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Blanche Ely High School

1201 NW 6 AVENUE, POMPANO BEACH 33060

Location Num	0361
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$23,335,150
Total Facilities Budget	\$21,665,436

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


### PRIMARY PROJECTS CURRENT STATUS: Construction

Primary Renovation: Construction in progress. Building 14 renovations are complete in the restrooms and concession areas. Building 2 STEM labs are nearing completion. Pending electrical closet design revisions and construction to address code compliance issues. Shower installation is pending for completion of the restroom scope of work. Building 1 HVAC work is in progress. Building 26 Science Lab work is in progress.

School Choice Enhancements:

COMPLETED 03/2020 - Voting authorized 4/6/2018 - Voting completed 06/2018 - Media Backdrop delivered 07/2018. Indoor tables and Bracket Kits with Activeboards delivered 01/2019. Projectors, tables and chairs delivered 08/2018. Science equipment delivered 11/2018. Digital Classroom Upgrades, (4) heart Models, and Podium delivered and installation complete 12/2018. , (117) laptops and adaptors delivered 6/2019. (1) Laptop 100e on order with the remaining SCEP balance.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **44% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2015	Q2 2016	Q4 2016	Q3 2017	Q1 2018	Q1 2019
New Planned	Q2 2015	Q2 2016	Q4 2016	Q3 2017	Q1 2018	Q3 2020
Actual/Forecast	6/1/2015	5/3/2016	11/2/2016	8/15/2018	10/5/2018	12/30/2021

#### SCOPE:

ADA Stage Lift	\$239,290
Additional Funding - Board Approved 04/17/18 (Item 1)	\$7,310,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.) incl. bldg #4	\$1,089,000
Fire Sprinklers	\$152,000
Gymnasium Accessibility	\$1,152,260
HVAC Improvements	\$6,202,000
IAQ & Fascia Replacement	\$2,791,886
Media Center improvements	\$668,000
Outdoor Dining Renovation	\$700,000
STEM Lab improvements	\$1,140,000

#### BUDGET:

FLAG: **S** - Delay Possible

#### COMMENTS:

Original contractual date of substantial completion is 8/1/2020. Delays continue to grow without a roofing sub-permit being approved. Without the roofing sub-permit, the project is forecasted to be completed December 2021.

FLAG KEY: **S**=Schedule **B**= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.



## Blanche Ely High School

### SMART Facilities Update by Project Cont.

#### Weight Room

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2017	Q1 2017	Q2 2017	Q2 2017	Q3 2017	Q4 2017
Actual/Forecast	3/8/2017	3/15/2017	4/4/2017	6/19/2017	7/20/2017	12/15/2017

<b>SCOPE:</b> Weight Room Renovation	<b>BUDGET:</b> \$121,000	<b>FLAG:</b> <b>COMMENTS:</b>
---	-----------------------------	----------------------------------

#### School Choice Enhancements\*

Phase: **99% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q2 2018	Q1 2020
Actual	11/2015	06/2018	03/2020

<b>SCOPE:</b> School Choice Enhancement	<b>BUDGET:</b> \$100,000	<b>FLAG:</b> <b>COMMENTS:</b> All items approved by voting process have been delivered and installed. (1) Lenovo computer is on order with remaining contingency portion of the SCEP funding.
--	-----------------------------	---

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Boulevard Heights Elementary School

7201 JOHNSON STREET, HOLLYWOOD 33024

Location Num	0971
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$4,070,000
Total Facilities Budget	\$3,890,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Bid advertisement is scheduled for September 2020.

School Choice Enhancements: Voting completed 5/7/18 - Two-way radios and a Poster Maker delivered 06/2018. Laptops carts, Printers, Outdoor Rugs and Laminator delivered 07/2018. (50) Laptops, (22) Mimio boards, Facilities Equipment and (2) electric strikes delivered and installed 08/2018. Marquee permitted 7/2/2019; pre-construction meeting held 10/14/2019; construction completed 01/2020.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: 5% Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2017	Q1 2018	Q3 2018	Q2 2019	Q4 2019	Q2 2020
New Planned	Q4 2017	Q1 2018	Q3 2018	Q4 2019	Q2 2020	Q2 2021
Actual/Forecast	10/2/2017	1/12/2018	3/14/2018	8/27/2019	Q1 2021	

#### SCOPE:

Art Room Renovation and Equipment	\$65,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,514,000
HVAC Improvements	\$1,596,000
Improvements to or Replacement of building 1	\$188,000
Improvements to or Replacement of building 4	\$291,000
Music Room Renovation	\$136,000

#### BUDGET:

FLAG: S - Delay Possible

#### COMMENTS:

Funding Year 1 thru 3 projects are to take priority for advertisement of bid. The project is funded under Year 4 and will be advertised after the funding Year 1 thru 3 projects that are prepared for advertisement.

FLAG KEY: S=Schedule B= Budget

S-Project Delayed=Schedule: Project has missed the planned milestone date for progressing to the next phase in the process.

S-Delay Possible=Schedule: Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

B=Budget: reflects a need for board approved increase in funding based on bid and/or change order results.

## Boulevard Heights Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **90% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q4 2017	Q2 2018	Q4 2018	Q4 2018
Actual	11/2017	05/2018		
<b>SCOPE:</b>				
School Choice Enhancement				
<b>BUDGET:</b>				
	\$100,000			
<b>FLAG:</b>	<b>S - Project Delayed</b>			
<b>COMMENTS:</b>	Marquee installation complete and the school is coordinating proposals			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Boyd H. Anderson High School

3050 NW 41 STREET, LAUDERDALE LAKES 33309

Location Num	1741
Board District	5
Board Member	Dr. Rosalind Osgood
ADEFP Budget*	\$8,209,340
Total Facilities Budget	\$7,513,340

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. The roofing reality check has been completed. Pending meeting with design firm to review changes to scope prior to advertising for bid.

School Choice Enhancements: COMPLETED 10/2018 - Voting authorized 2/1/18. Voting completed 3/8/18 - Recordex delivered and installed 06/2018. Sound system for the Gymnasium and laptop cart with 30 laptops delivered 06/2018. Portable Sound System, and roof for visitor's dugout delivered 07/2018. Lockers and Golf Carts delivered 08/2018. Gym Wall Pads delivered 10/2018.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **5% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2016	Q4 2016	Q2 2017	Q1 2018	Q3 2018	Q3 2019
New Planned	Q3 2016	Q4 2016	Q2 2017	Q2 2019	Q4 2019	Q2 2021
Actual/Forecast	9/19/2016	11/1/2016	4/25/2017	2/10/2020	Q4 2020	

#### SCOPE:

ADA renovations related to educational adequacy	\$388,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$2,580,000
HVAC Improvements	\$543,508
Safety / Security Upgrade	\$77,000
STEM Lab improvements	\$1,380,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred in the permitting process of the design phase. The design firm had taken an average of two months to submit each of the first two design drawing sets and the fifth set for review by the Building Department. The design firm took three months to submit the fourth revision. Remedy: The owner will be enforcing terms of the contract for delays and multiple resubmissions. The project has received a Letter of Recommendation to Permit. Delays from the design phase are not forecasted to be recovered.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Boyd H. Anderson High School

### SMART Facilities Update by Project Cont.

#### HVAC Improvements

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout	
Planned	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	N/A	N/A	N/A

<b>SCOPE:</b> HVAC Improvements - Chiller Replacement	<b>BUDGET:</b> \$305,492	<b>FLAG:</b> <b>COMMENTS:</b>
--	-----------------------------	----------------------------------

#### Media Center Reconstruction

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout	
Planned	Q2 2015	Q2 2015	Q2 2015	Q3 2015	Q3 2016	Q1 2017	Q3 2017
Actual/Forecast	5/8/2015	5/21/2015	6/18/2015	6/29/2015	8/31/2016	3/6/2017	8/16/2017

<b>SCOPE:</b> Renovation of the existing Media Center - re-Construction Phase	<b>BUDGET:</b> \$1,772,548	<b>FLAG:</b> <b>COMMENTS:</b>
--	-------------------------------	----------------------------------

#### Weight Room

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout	
Planned	Q2 2017	Q2 2017	Q3 2017	Q3 2017	Q3 2017	Q2 2018	Q2 2018
Actual/Forecast	5/5/2017	5/12/2017	7/13/2017	1/12/2018	1/19/2018	4/22/2018	4/23/2018

<b>SCOPE:</b> Weight Room Renovation	<b>BUDGET:</b> \$121,000	<b>FLAG:</b> <b>COMMENTS:</b>
---	-----------------------------	----------------------------------

#### Media Center Demolition

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout	
Planned	Q2 2015	Q2 2015	Q2 2015	Q3 2015	Q3 2015	Q4 2015	Q4 2016
Actual/Forecast	5/8/2015	5/21/2015	6/18/2015	6/29/2015	6/29/2015	8/16/2016	11/10/2016

<b>SCOPE:</b> Renovation of the existing Media Center - Demolition phase	<b>BUDGET:</b> \$245,792	<b>FLAG:</b> <b>COMMENTS:</b>
---	-----------------------------	----------------------------------

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Boyd H. Anderson High School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:		PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2016	Q1 2018	Q4 2018	Q4 2018
Actual	12/2016	03/2018	10/2018	10/2018
SCOPE:		BUDGET:	FLAG:	
School Choice Enhancement		\$100,000	COMMENTS:	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Bright Horizons Center

3901 NE 1ST TERRACE, DEERFIELD BEACH 33064

Location Num	0871
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$4,046,871
Total Facilities Budget	\$3,656,100

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

## PRIMARY PROJECTS CURRENT STATUS: Construction

Primary Renovation: Construction in progress. Fire Alarm and Fire Sprinkler scope in progress. Roofing submittals are being revised and resubmitted.

School Choice Enhancements: Voting completed 5/3/2018 - Items voted - Technology (7 Recordex) delivered 06/2018. Preliminary approvals received from District ADA Manager and playground Inspector for the shade; vendor did not deliver, PO cancelled on 8/2019; proposals are in progress. New PO request issued 10/31/2019 for another vendor. Digital Marquee permit received 11/2019; pre-construction meeting TBD.

## SMART Facilities Update By Project



### Primary Renovation

Phase: **20% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2016	Q4 2016	Q2 2017	Q3 2017	Q2 2018	Q2 2019
New Planned	Q4 2016	Q4 2016	Q2 2017	Q1 2019	Q3 2019	Q4 2020
Actual/Forecast	10/20/2016	11/25/2016	7/26/2017	2/4/2019	8/29/2019	6/30/2020

### SCOPE:

Additional Funding - Board Approved 07/23/19 (JJ-4)	\$1,893,100
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$864,000
Fire Alarm	\$42,000
Fire Sprinklers	\$654,000
HVAC Improvements	\$103,000

### BUDGET:

### FLAG:

### COMMENTS:

Original contractual date of substantial completion is 3/2/2020 but construction is estimated to be completed in Q2 2020 pending receipt of the sub-permit.

## Bright Horizons Center

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **17% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q4 2017	Q2 2018	Q4 2018	Q4 2018
Actual	11/2017	05/2018		
<b>SCOPE:</b>				
School Choice Enhancement				
<b>BUDGET:</b>				
\$100,000				
<b>FLAG:</b>	<b>S - Project Delayed</b>			
<b>COMMENTS:</b>	Pending completion of the marquee sign.			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Broadview Elementary School

1800 SW 62 AVENUE, NORTH LAUDERDALE 33068

Location Num	0811
Board District	4
Board Member	Lori Alhadeff
ADEFP Budget*	\$3,387,386
Total Facilities Budget	\$2,891,386

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Pending roofing reality check. Bid advertisement is scheduled for April 2020.

School Choice Enhancements: COMPLETED 02/2020 - Voting completed 11/17/16. Proposals for additional rugs will be finalized once the playground upgrades are delivered and installed. Digital Marquee delivered and installed 09/2018. Classroom rugs delivered 03/2019. Playground upgrades' permit issued 1/2019. Pre-Construction meeting held 3/4/2019; playground equipment delivered to the site; construction complete 6/2019. (32) Laptops, (10) Mini HDMI, (20) Adapters delivered 02/2020.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: 5% Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2015	Q4 2015	Q3 2016	Q4 2017	Q2 2018	Q2 2020
New Planned	Q2 2015	Q4 2015	Q3 2016	Q2 2019	Q4 2019	Q1 2021
Actual/Forecast	5/2/2015	12/8/2015	8/9/2016	2/6/2020	Q3 2020	

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$63,228
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.) - Roofing	\$945,772
Conversion of Existing Space to Music and/or Art Lab(s)	\$169,000
Electrical Improvements	\$56,329
Fire Alarm	\$252,578
Fire Sprinklers	\$718,479
HVAC Improvements	\$264,000
Media Center improvements	\$186,000
Music Room Renovation	\$136,000

#### BUDGET:

FLAG: S - Project Delayed

#### COMMENTS:

Reason: Delays have occurred in the permitting phase of the design process. Multiple revisions have been required by the design firm in order to achieve a permit. Remedy: The owner will be enforcing terms of the contract for delays and multiple resubmissions. The project has received a Letter of Recommendation to Permit. Delays from the design phase are not forecasted to be recovered.

FLAG KEY: S=Schedule B= Budget

S-Project Delayed=Schedule: Project has missed the planned milestone date for progressing to the next phase in the process.

S-Delay Possible=Schedule: Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

B=Budget: reflects a need for board approved increase in funding based on bid and/or change order results.

## Broadview Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **100% Complete**

<b>SCHEDULE:</b>	<b>PH:1 Planning/Design</b>		<b>PH:2 Implement</b>	<b>PH:3 Complete</b>
Planned	Q1 2015	Q4 2016	Q1 2020	Q1 2020
Actual	01/2015	11/2016	02/2020	02/2020
<b>SCOPE:</b>	<b>BUDGET:</b>		<b>FLAG:</b>	
School Choice Enhancement	\$100,000		<b>COMMENTS:</b>	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Broward Estates Elementary School

441 NW 35 AVENUE, LAUDERHILL 33311

Location Num	0501
Board District	5
Board Member	Dr. Rosalind Osgood
ADEFP Budget*	\$3,016,000
Total Facilities Budget	\$2,863,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Project advertised for bids in March 2020.

School Choice Enhancements: Meeting held with staff, ballot development in progress.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **10% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2017	Q3 2017	Q2 2018	Q1 2019	Q2 2019	Q1 2020
New Planned	Q3 2017	Q3 2017	Q2 2018	Q3 2019	Q1 2020	Q1 2021
Actual/Forecast	5/1/2017	7/20/2017	3/12/2018	7/29/2019	Q3 2020	

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG: S - Project Delayed</b>
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,812,000	<b>COMMENTS:</b> Funding Year 1 thru 3 projects are to take priority for advertisement of bid. The project is funded under Year 4. Advertisement for bids took place in March 2020 with all available Year 1 thru 3 projects already advertised.
HVAC Improvements	\$951,000	

#### School Choice Enhancements\*

Phase: **25% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2017	TBD	TBD
Actual	11/2017		

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
School Choice Enhancement	\$100,000	<b>COMMENTS:</b> Planned date for Implementation phase shown as TBD will be provided after voting process has been completed by the school community.

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## C. Robert Markham Elementary School

1501 NW 15 AVENUE, POMPANO BEACH 33069

Location Num	1671
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$9,510,000
Total Facilities Budget	\$9,259,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. CM firm has been terminated due to inability to reach an agreement. Pending re-negotiations with design firm to move forward with a Design/Bid/Build delivery method.

School Choice Enhancements: COMPLETED 08/2019 - Voting authorized 5/8/2018 - Voting completed 6/2/18 - The majority of the office furniture delivered 09/2018 (students desks, chairs, cafeteria tables, front office). Remaining office furniture (students desks, chairs, cafeteria tables, front office and more) delivered 10/2018. Water bottle filling stations construction completed 10/2018. Extra (13) Chairs and (8) Tables delivered 02/2019. (2) chairs delivered 08/2019.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **5% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2017	Q1 2017	Q4 2017	Q3 2018	Q1 2019	Q1 2020
New Planned	Q1 2017	Q1 2017	Q4 2017	Q3 2019	Q4 2019	Q3 2021
Actual/Forecast	1/10/2017	2/7/2017	11/15/2017	7/30/2019	Q3 2020	

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$656,000
Fire Alarm	\$294,000
Fire Sprinklers	\$310,000
HVAC Improvements	\$303,000
Improvements to or Replacement of building 1	\$7,440,000

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays occurred during the bid and award phase. Extensive negotiations were required in order to provide a quality GMP acceptable to the District. Remedy: The CM firm has been terminated due to inability to reach an agreement, and the project will progress with a Design/Bid/Build delivery method. Correction: The percent complete of the bid and award phase has been reduced to 5% to take into account the termination of the CM firm.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## C. Robert Markham Elementary School

### SMART Facilities Update by Project Cont.

#### HVAC Improvements

Phase: **100%** Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout	
Planned	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	N/A	N/A	3/21/2018

<b>SCOPE:</b> HVAC Improvements - Chiller Replacement	<b>BUDGET:</b> \$156,000	<b>FLAG:</b> <b>COMMENTS:</b>
--	-----------------------------	----------------------------------

#### School Choice Enhancements\*

Phase: **100%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete	
Planned	Q4 2017	Q2 2018	Q1 2019	Q1 2019
Actual	11/2017	06/2018	08/2019	08/2019

<b>SCOPE:</b> School Choice Enhancement	<b>BUDGET:</b> \$100,000	<b>FLAG:</b> <b>COMMENTS:</b>
--	-----------------------------	----------------------------------

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Castle Hill Elementary School

2640 NW 46 AVENUE, LAUDERHILL 33313

Location Num	1461
Board District	5
Board Member	Dr. Rosalind Osgood
ADEFP Budget*	\$4,059,030
Total Facilities Budget	\$3,776,030

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. Roofing, Media Center, and Fire Alarm scope is in progress. A Notice of Non-Conformance and a Notice to Cure has been issued. The contractor is currently behind schedule.

School Choice Enhancements: COMPLETED 03/2020 - Voting completed 12/2016. Mimio boards delivered 3/2017. Murals completed 09/2017. Cafeteria Sound system, projector delivered 08/2017. (4)TVs, and a TV Production studio delivered and installed 01/2018. Classroom furniture delivered 06/2018. Marquee installation completed 08/2018. Projector screen delivered 8/2019.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **50% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2017	Q1 2017	Q2 2017	Q4 2017	Q2 2018	Q2 2019
New Planned	Q1 2017	Q1 2017	Q2 2017	Q4 2017	Q2 2018	Q2 2019
Actual/Forecast	3/6/2017	3/10/2017	4/20/2017	3/19/2018	7/18/2018	6/9/2020

SCOPE:	BUDGET:
Additional Funding - Board Approved 05/22/18 (JJ-1)	\$1,567,030
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,141,000
Fire Alarm	\$293,000
Fire Sprinklers	\$13,000
HVAC Improvements	\$279,950
Media Center improvements	\$282,000

**FLAG: S - Project Delayed**

#### COMMENTS:

Original contractual date of substantial completion is 1/25/2019. Reason: Delays have occurred during the construction phase. The contractor was delayed for a month at the principal's request. Additionally, there were delays of six months in receiving a roofing sub-permit. Remedy: A Notice to Cure has been issued. Currently re-evaluating the contractor performance. Update: The contractor continues to be delayed. Most recent recovery schedule showed substantial completion on 5/12/2020. Delays are expected to continue with May 2020 not achievable.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.



## Castle Hill Elementary School

### SMART Facilities Update by Project Cont.

#### Cooling Tower Replacement

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	6/1/2016	7/1/2016 6/7/2017

<b>SCOPE:</b> HVAC Improvements - Cooling Tower Replacement	<b>BUDGET:</b> \$100,050	<b>FLAG:</b> <b>COMMENTS:</b>
--	-----------------------------	----------------------------------

#### School Choice Enhancements\*

Phase: **99% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q4 2016	Q1 2020
Actual	11/2015	12/2016	03/2020

<b>SCOPE:</b> School Choice Enhancement	<b>BUDGET:</b> \$100,000	<b>FLAG:</b> <b>COMMENTS:</b> All items approved by voting process have been delivered and installed. School is determining how to spend the remaining funding from the contingency portion of the SCEP funding.
--	-----------------------------	--

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Central Park Elementary School

777 N NOB HILL ROAD, PLANTATION 33322

Location Num	2641
Board District	6
Board Member	Laurie Rich Levinson
ADEFP Budget*	\$5,493,475
Total Facilities Budget	\$5,027,475

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Bid opening has occurred. Pending Board award.

School Choice Enhancements: Voting completed on 11/28/16. Computer carts and printers delivered on 3/2017. Classroom furniture delivered 4/2017. Science lab materials delivered 06/2017. Classroom furniture and bulletin boards delivered and installed 8/9/17. Carpet replaced in FISH 301 and completed 08/2019. Blinds completed 09/2019. Coordinating additional proposals.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **25% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2016	Q3 2016	Q1 2017	Q4 2017	Q1 2018	Q1 2019
New Planned	Q2 2016	Q3 2016	Q1 2017	Q1 2019	Q2 2019	Q4 2020
Actual/Forecast	5/2/2016	7/26/2016	1/13/2017	10/1/2019	Q2 2020	

#### SCOPE:

ADA Stage Lift	\$119,475
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,361,000
Conversion of Existing Space to Music and/or Art Lab(s)	\$169,000
Fire Sprinklers	\$982,000
HVAC Improvements	\$2,100,000
Music Room Renovation	\$136,000
Safety / Security Upgrade	\$60,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred in the design phase related to permitting. The design firm has required an above average amount of submissions of the Construction Documents prior to receiving a Letter of Recommendation to permit. Remedy: The delays are not anticipated to be recovered. The construction schedule will be closely monitored to avoid further delays. Update: The project is pending Board award of the contract.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Central Park Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **79% Complete**

SCHEDULE:	<div><div>PH:1 Planning/Design</div><div>PH:2 Implement</div><div>PH:3 Complete</div></div>			
	Planned	Q1 2016	Q4 2016	TBD
	Actual	01/2016	11/2016	
SCOPE:				
School Choice Enhancement				
BUDGET:				
\$100,000				
FLAG:	<div>COMMENTS:</div> <div>Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.</div>			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Challenger Elementary School

5703 NW 94 AVENUE, TAMARAC 33321

Location Num	3771
Board District	4
Board Member	Lori Alhadeff
ADEFP Budget*	\$1,835,000
Total Facilities Budget	\$1,449,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Bid opening has occurred. Pending Board award to a contractor.

School Choice Enhancements: Voting authorized 5/13/18 - Voting results received 7/2/18 - (5) iPads delivered 01/2019. (2) Playground Shades covering and Marquee are on order. (40) Lenovo 300e - (3) Lenovo ThinkPad - (2) Lenovo M820z delivered 03/2019. Marquee permitted 7/8/2019; pre-construction meeting held 10/14/2019; construction completed 02/2020. (2) shade structures on order.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **25% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2017	Q3 2017	Q2 2018	Q4 2018	Q2 2019	Q1 2020
New Planned	Q3 2017	Q3 2017	Q2 2018	Q3 2019	Q1 2020	Q1 2021
Actual/Forecast	5/1/2017	7/20/2017	2/6/2018	8/16/2019	Q3 2020	

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$857,000
Conversion of Existing Space to Music and/or Art Lab(s)	\$169,000
Fire Alarm	\$42,000
HVAC Improvements	\$145,000
Music Room Renovation	\$136,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Funding Year 1 thru 3 projects are to take priority for advertisement of bid. The project is funded under Year 4 and has been advertised after the available funding Year 1 thru 3 projects were advertised.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Challenger Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **47% Complete**

SCHEDULE:	<div><div>PH:1 Planning/Design</div><div>PH:2 Implement</div><div>PH:3 Complete</div></div>			
	Planned	Q4 2017	Q3 2018	TBD
	Actual	11/2017	07/2018	
SCOPE:				
School Choice Enhancement				
BUDGET:				
\$100,000				
FLAG:	<div>COMMENTS:</div> <div>Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.</div>			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Chapel Trail Elementary School

19595 TAFT STREET, PEMBROKE PINES 33029

Location Num	2961
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$5,146,650
Total Facilities Budget	\$4,638,436

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. Submittals in progress.

School Choice Enhancements: Voting completed 10/13/16. Student laptops and stage curtains delivered 2/2017. Playground shades permitted; construction began 10/2018. (1) bus loop shade completed 12/2018. Plan change submitted and approved for the second shade structure 12/2018; construction scheduled for 03/2019. Plan change permitted 04/2019.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **8% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2017	Q1 2017	Q1 2017	Q3 2017	Q2 2018	Q1 2019
New Planned	Q1 2017	Q1 2017	Q1 2017	Q2 2019	Q3 2019	Q3 2020
Actual/Forecast	1/11/2017	1/11/2017	3/15/2017	5/22/2019	1/22/2020	1/2/2021

#### SCOPE:

Additional Funding - Board Approved 11/06/19 (JJ-2)

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

Fire Alarm

HVAC Improvements

#### BUDGET:

\$2,850,436

\$1,169,000

\$42,000

\$172,000

#### FLAG: S - Delay Possible

#### COMMENTS:

Delays occurred during bid and award. Funding Year 1 thru 3 projects are to take priority for advertisement of bid. The project is funded under Year 4 and was advertised after the available Funding Year 1 thru 3 projects were advertised. Original contractual date of substantial completion is 1/27/2021. Project is currently on track.

#### HVAC Improvements

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	N/A	3/23/2018

#### SCOPE:

HVAC Improvements - Chiller Replacement

#### BUDGET:

\$305,000

#### FLAG:

#### COMMENTS:

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.


**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Chapel Trail Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

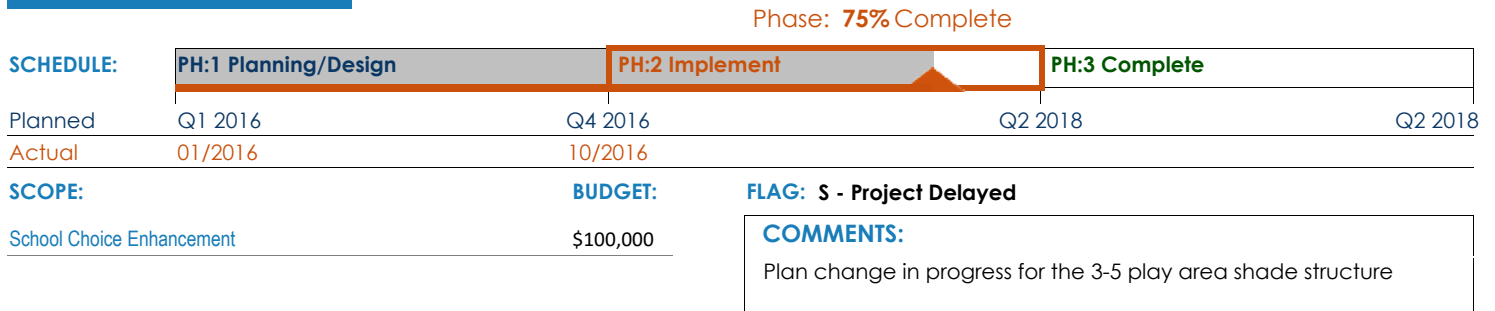

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Charles Drew Elementary School

1000 NW 31 AVENUE, POMPANO BEACH 33060

Location Num	3221
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$3,310,000
Total Facilities Budget	\$3,117,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. Building Department is currently reviewing the second submission.

School Choice Enhancements: COMPLETED 01/2019 - Voting completed 11/16/17 - Portable PA system and trash cans delivered 01/2018. Murals complete 02/2018. Two-way radios and (20) Projectors delivered 2/2018. Golf carts, Cafeteria sound system, floor mats, traffic cones and stage curtains delivered 03/2018. Office Furniture delivered 05/2018. Picnic Tables delivered 01/2019.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **96% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2016	Q3 2016	Q2 2017	Q4 2017	Q3 2018	Q3 2019
New Planned	Q3 2016	Q3 2016	Q2 2017	Q3 2019	Q4 2019	Q1 2021
Actual/Forecast	8/8/2016	9/7/2016	3/30/2017	Q2 2020		

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$138,000
Fire Alarm	\$293,000
Fire Sprinklers	\$694,000
HVAC Improvements	\$1,892,000

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred during design due to multiple submissions to close review comments prior to permit review. Remedy: Comments have been closed and the project has been submitted for permit review. The owner will be enforcing terms of the contract for delays.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.



## Charles Drew Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **100%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q4 2017	Q2 2018
Actual	11/2015	11/2017	01/2019
SCOPE:	BUDGET:		
School Choice Enhancement	\$100,000		
	COMMENTS:		

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Charles Drew Family Resource Center

2600 NW 9TH COURT, POMPANO BEACH 33060

Location Num	0301
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$3,496,000
Total Facilities Budget	\$3,378,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. Design firm currently addressing Building Department review comments in order to submit for a second time to permit application.

School Choice Enhancements: COMPLETED 05/2018 - Voting results received 6/1/17. Voting was completed prior to OFC's approval. Budget evaluated and approved. Front Office Renovation, Microphones and office furniture. (8) Elmo Boards, (6) speakers, printers and outdoor benches complete 08/17. Twelve (12) ThinkPad's and a printer delivered 10/2017.

### SMART Facilities Update By Project



#### Primary Renovation

 Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2016	Q3 2016	Q2 2017	Q2 2017	Q3 2018	Q3 2019
New Planned	Q3 2016	Q3 2016	Q2 2017	Q3 2019	Q4 2019	Q1 2021
Actual/Forecast	9/19/2016	11/1/2016	4/6/2017	Q2 2020		

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,173,000
HVAC Improvements	\$225,000
Improvements to or Replacement of building 3	\$557,000
Improvements to or Replacement of building 5	\$575,000
Improvements to or Replacement of building 6	\$557,000
Media Center improvements	\$191,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred during design due to multiple submissions to close review comments prior to permit review. Remedy: Comments have been closed and the project has been submitted for permit review. The owner will be enforcing terms of the contract for delays.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Charles Drew Family Resource Center

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete	
Planned	Q4 2016	Q2 2017	Q1 2018	Q1 2018
Actual	12/2016	06/2017	05/2018	05/2018
SCOPE:				
School Choice Enhancement				
BUDGET:				
\$100,000				
FLAG:				
COMMENTS:				

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Charles W. Flanagan High School

12800 TAFT STREET, PEMBROKE PINES 33028

Location Num	3391
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$17,029,361
Total Facilities Budget	\$15,847,361

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Complete

Primary Renovation: Construction in progress. All work has been completed. The project is pending final inspections in order to closing out the project.

School Choice Enhancements: Voting authorized 3/20/2019. Voting results received 8/29/2019. Floor scrubber, hedger, trimmer, blower, (2) ID machines, (5) recordex, digital 4'x8' marquee, (4) gold carts, (15) two-way radios delivered 11/2019. (10) Two-way radio batteries delivered 11/2019. (4) Golf Carts delivered 01/2020.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **10%Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2016	Q4 2016	Q2 2017	Q1 2018	Q4 2018	Q4 2019
New Planned	Q3 2016	Q4 2016	Q2 2017	Q1 2018	Q4 2018	Q4 2019
Actual/Forecast	9/9/2016	11/1/2016	4/27/2017	8/7/2018	10/19/2018	1/3/2020

SCOPE:	BUDGET:	FLAG:
Additional Funding - Board Approved 09/05/18 (JJ-2)	\$6,793,361	COMMENTS:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,357,000	
CR Addition to allow for removal of portable bldgs	\$6,124,000	
HVAC Improvements	\$1,052,000	

#### Weight Room

Phase: **100%Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q3 2017	Q3 2017	Q4 2017	Q1 2018
Actual/Forecast	5/5/2017	5/12/2017	7/13/2017	12/8/2017	1/10/2018	2/4/2018

SCOPE:	BUDGET:	FLAG:
Weight Room Renovation	\$121,000	COMMENTS:

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Charles W. Flanagan High School

### SMART Facilities Update by Project Cont.

#### Track

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	10/3/2016	11/18/2016 11/18/2016

<b>SCOPE:</b> Track Resurfacing	<b>BUDGET:</b> \$300,000	<b>FLAG:</b> <b>COMMENTS:</b>
------------------------------------	-----------------------------	----------------------------------

#### School Choice Enhancements\*

Phase: **70% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2016	Q3 2019	TBD
Actual	12/2016	08/2019	TBD

<b>SCOPE:</b> School Choice Enhancement	<b>BUDGET:</b> \$100,000	<b>FLAG:</b> <b>COMMENTS:</b> Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.
--	-----------------------------	--

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Coconut Creek Elementary School

500 NW 45 AVENUE, COCONUT CREEK 33066

Location Num	1421
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$5,503,761
Total Facilities Budget	\$5,144,761

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Complete

Primary Renovation: Construction in substantial completion. Final inspections are pending.

School Choice Enhancements: COMPLETED 02/2019 - Voting completed 2/19/16 - 38 TVs delivered 12/2017; installed 02/2018. Additional TV delivered 02/2018. Playground installation completed 04/2018. TV delivered 08/2018; installed 11/2018. Outdoor benches delivered 09/2018. Table on order 02/2019.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: 10% Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2015	Q4 2015	Q3 2016	Q1 2017	Q3 2017	Q3 2018
New Planned	Q4 2015	Q4 2015	Q3 2016	Q1 2017	Q3 2017	Q1 2019
Actual/Forecast	10/29/2015	12/8/2015	8/25/2016	5/4/2017	2/26/2018	2/28/2020

#### SCOPE:

Additional Funding - Board Approved 12/19/17 (JJ-14)	\$517,143
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,055,000
Fire Alarm	\$294,000
Fire Sprinklers	\$699,000
Media Center improvements	\$274,000
Replace existing unit ventilators (appr. 43 CRs) with new unit ventilators.	\$2,205,618

#### BUDGET:

#### FLAG:

#### COMMENTS:

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Coconut Creek Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q1 2016	Q1 2018
Actual	11/2015	02/2016	02/2019
SCOPE:	BUDGET:		
School Choice Enhancement	\$100,000		
	FLAG:		
	COMMENTS:		

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Coconut Creek High School

1400 NW 44 AVENUE, COCONUT CREEK 33066

Location Num	1681
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$5,985,907
Total Facilities Budget	\$4,523,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. Building Department is currently reviewing the first submission.

School Choice Enhancements: COMPLETED 03/2020 - Voting authorized 2/9/2018. Voting completed 3/2/2018. Projectors delivered 05/2018. Auditorium Sound System, Cafeteria Tables delivered and installed 08/2018. Laptops carts and (30) laptops delivered 09/2018. Projector screen delivered 03/2019. Additional Cafeteria Tables on order. Auditorium Projector delivered 06/2019. (4) additional cafeteria tables delivered 8/2019. (1) Laptop 100E ordered with the remaining funds.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2016	Q2 2016	Q3 2016	Q4 2017	Q2 2018	Q2 2019
New Planned	Q1 2016	Q2 2016	Q3 2016	Q4 2019	Q2 2020	Q3 2021
Actual/Forecast	2/10/2016	4/19/2016	9/23/2016	Q2 2020		

#### SCOPE:

Auditorium Accessibility	\$250,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$686,000
Fire Alarm	\$1,174,000
HVAC Improvements	\$814,000
Media Center improvements	\$600,000
Safety / Security Upgrade	\$53,000
STEM Lab improvements	\$725,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred during the design phase. The design firm has not met the deadlines of the design deliverables. Remedy: The owner will be enforcing terms of the contract for delays.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Coconut Creek High School

### SMART Facilities Update by Project Cont.

#### Weight Room

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q3 2017	Q3 2017	Q3 2017	Q1 2018
Actual/Forecast	4/14/2017	4/21/2017	7/13/2017	8/1/2017	10/19/2017	1/17/2018

<b>SCOPE:</b> Weight Room Renovation	<b>BUDGET:</b> \$121,000	<b>FLAG:</b> <b>COMMENTS:</b>
---	-----------------------------	----------------------------------

#### School Choice Enhancements\*

Phase: **99% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2016	Q1 2018	Q3 2020
Actual	01/2016	03/2018	03/2020

<b>SCOPE:</b> School Choice Enhancement	<b>BUDGET:</b> \$100,000	<b>FLAG:</b> <b>COMMENTS:</b> All items approved by voting process have been delivered and installed. (1) Lenovo computer is on order with funding from the contingency portion of the SCEP funding.
--	-----------------------------	--

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Coconut Palm Elementary School

13601 MONARCH LAKES BOULEVARD, MIRAMAR 33027

Location Num	3741
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$1,599,000
Total Facilities Budget	\$1,156,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. Design firm currently addressing Building Department comments prior to submitting the sixth time for permit application.

School Choice Enhancements: Voting completed 9/20/16. PIP rubber surfacing completed 02/2017. Basketball shade structure permitted 07/2018; installed 01/2019. Aiphone submaster station installed 04/2019. (1) Recordex and (2) AC adapters delivered 04/2019. Laptops delivered 06/2019.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **99% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q1 2019	Q2 2019	Q1 2020	Q2 2020
New Planned	Q1 2018	Q2 2018	Q1 2019	Q1 2020	Q2 2020	Q2 2021
Actual/Forecast	8/1/2017	10/6/2017	3/22/2018	Q2 2020		

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

Fire Alarm

HVAC Improvements

#### BUDGET:

\$746,000

\$42,000

\$268,000

#### FLAG: S - Project Delayed

#### COMMENTS:

Reason: Delays occurred during the design phase related to permitting. Additional testing on the roofing system was required in order to submit for a sixth review to the Building Department. Remedy: The testing has been completed and the sixth submission is pending.

FLAG KEY: S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Coconut Palm Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:		PH:1 Planning/Design		PH:2 Implement		PH:3 Complete	
Planned	Q1 2015		Q3 2016		Q2 2018		Q2 2018
Actual	11/2015		09/2016		07/2019		07/2019
SCOPE:		BUDGET:		FLAG:			
School Choice Enhancement		\$100,000		COMMENTS:			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Colbert Museum Magnet

(f.k.a. Colbert Elementary School)

2702 FUNSTON ST., HOLLYWOOD 33020

Location Num	0231
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$1,921,903
Total Facilities Budget	\$1,690,903

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. Roofing submittals are in progress. Lighting installation is complete, and the fire alarm panel is on order.

School Choice Enhancements: Principal advised that the voting was completed prior to her transfer on July 1st, 2017. Laptops and laptop carts delivered 11/2017. Recordex, Camera, Microphone, and Media Center chairs final delivered 01/2018. Shade structure permitted 09/2018; construction began 02/2019; plan change permitted 03/2019, resuming of construction TBD. Digital marquee: permit issued 03/2019; marquee in fabrication. Pre-construction meeting held 5/7/2019; permitting in progress.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: <b>42% Complete</b>						
SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2017	Q1 2017	Q2 2017	Q4 2017	Q3 2018	Q2 2019
New Planned	Q1 2017	Q1 2017	Q2 2017	Q1 2019	Q2 2019	Q1 2020
Actual/Forecast	2/1/2017	2/1/2017	4/19/2017	12/18/2018	4/18/2019	9/30/2020

#### SCOPE:

Additional Funding - Board Approved 02/20/19 (JJ-3)	\$834,903
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$323,000
HVAC Improvements	\$368,000
Safety / Security Upgrade	\$65,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Original contractual date of substantial completion is 12/5/2019. Reason: Delays occurred during construction related to the roofing sub-permit. The project continues to be delayed until the roofing sub-permit is received. Remedy: The construction is estimated to be completed in Q3 2020 pending receipt of the sub-permit.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Colbert Museum Magnet

(f.k.a. Colbert Elementary School)

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **72% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q1 2015	Q2 2017	Q1 2018	Q1 2018
Actual	01/2015	06/2017		
<b>SCOPE:</b>				
School Choice Enhancement				
<b>BUDGET:</b>				
	\$100,000			
<b>FLAG:</b>	<b>S - Project Delayed</b>			
<b>COMMENTS:</b>	Playground shade structure construction is complete. Marquee is in fabrication.			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Collins Elementary School

1050 NW 2 STREET, DANIA 33004

Location Num	0331
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$2,040,000
Total Facilities Budget	\$1,874,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. CM firm has received bids in preparation of the GMP which are over the continuing contract construction cost limits. The Fire Alarm scope separation was rejected by the Board. The CM firm will be removed from the project and the project will move forward advertising for bids.

School Choice Enhancements: COMPLETED 03/2020 - Voting authorized 3/20/18 - Voting completed 05/2018 - Document Cameras delivered 06/2018. (10) Printers, (1) Recordex and outdoor bulleting boards delivered and installed 08/2018. Two-way radios, projector screen, Murals, (100) laptops, (7) ThinkPad's delivered and installed 09/2018. Recordex delivered 5/2019. Digital marquee permit issued 7/2/2019; pre-construction meeting held 8/2019; Construction began 12/2019; final inspection in progress.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **25% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2017	Q3 2017	Q3 2017	Q2 2018	Q3 2018	Q3 2019
New Planned	Q3 2017	Q3 2017	Q3 2017	Q2 2019	Q4 2019	Q4 2020
Actual/Forecast	8/1/2017	8/18/2017	10/31/2017	8/27/2019	Q2 2020	Q1 2021

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$473,000
Electrical Improvements	\$281,000
Fire Alarm	\$294,000
Fire Sprinklers	\$10,000
HVAC Improvements	\$378,000
Media Center improvements	\$77,000
Restroom Renovations	\$119,000
Safety / Security Upgrade	\$142,000

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays occurred during Bid and Award. The CM firm received bids which are over the \$2,000,000 threshold for continuing contracts. Remedy: The Board rejected the separation of the Fire Alarm scope of work. The project will move forward advertising for bids.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.



## Collins Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **98% Complete**

SCHEDULE:		PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned		Q4 2017	Q2 2018	Q1 2019
Actual		11/2017	05/2018	03/2020
SCOPE:		BUDGET:		FLAG:
School Choice Enhancement		\$100,000		COMMENTS:
				All items approved by voting process have been delivered and installed. Budget reconciliation is in progress.

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Cooper City Elementary School

5080 SW 92 AVENUE, COOPER CITY 33328

Location Num	1211
Board District	6
Board Member	Laurie Rich Levinson
ADEFP Budget*	\$1,350,000
Total Facilities Budget	\$967,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. CSMP term contracts have expired. Project is on hold until new CSMP contractors are available.

School Choice Enhancements: Originally a Year 5 school accelerated to Year 4 following Board approval. Kick-off meeting held with 2/6/2018 - SAC meeting attended 12/28/18 - Voting completed 2/1/2019. (1) Golf cart delivered 04/2019. Waterproof Vinyl floor installation complete. Furniture for the reception area, Principal's office and chairs on order. Wind screen, (80) Lenovo 300e, (4) EarthWalk Cart, (540) New Cart Cable Management, (10) Motorola Digital Portable Radios, FISH 101 delivered 02/2020. Signage TV, (2) Desktops, Wind Screen, Signage TV Installation on order.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **10% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q1 2019	Q3 2019	Q1 2020	Q3 2020
New Planned	Q1 2018	Q2 2018	Q1 2019	Q4 2019	Q1 2020	Q2 2021
Actual/Forecast	9/28/2017	2/6/2018	8/7/2018	2/12/2020	Q3 2020	

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$118,000
Fire Alarm	\$294,000
Fire Sprinklers	\$10,000
HVAC Improvements	\$163,000
Media Center improvements	\$282,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays occurred in design due to an above average amount of submissions to the Building Department for permit review. Remedy: The Letter of Recommendation for Permit has been received. Pending new CSMP contractor list.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Cooper City Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **70% Complete**

SCHEDULE:	<div><div>PH:1 Planning/Design</div><div>PH:2 Implement</div><div>PH:3 Complete</div></div>			
	Planned	Q4 2018	Q1 2019	TBD
	Actual	03/2018	02/2019	
SCOPE:				
School Choice Enhancement				
BUDGET:				
\$100,000				
FLAG:				
<div>COMMENTS:</div> <div>Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.</div>				

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Cooper City High School

9401 STIRLING ROAD, COOPER CITY 33328

Location Num	1931
Board District	6
Board Member	Laurie Rich Levinson
ADEFP Budget*	\$12,055,872
Total Facilities Budget	\$8,830,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Design**

Primary Renovation: 100% Construction Drawings in progress.

School Choice Enhancements: Principal's letter initiated 11/30/2018 for Year 5 group. Kick-off meeting held 2/12/2019. Ballot approved for voting 02/2020.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **85% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2017	Q4 2017	Q3 2018	Q1 2019	Q4 2019	Q2 2021
New Planned	Q4 2017	Q4 2017	Q3 2018	Q2 2020	Q4 2020	Q2 2022
Actual/Forecast	11/13/2017	12/13/2017	7/17/2018	Q3 2020		

SCOPE:	BUDGET:
Auditorium Accessibility	\$250,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$844,000
Electrical Improvements	\$428,000
Fire Sprinklers	\$3,583,000
HVAC Improvements	\$2,208,000
Improvements to or Replacement of building 5	\$238,000
Safety / Security Upgrade	\$57,000
STEM Lab improvements	\$1,001,000

**FLAG: S - Delay Possible**

#### COMMENTS:

Delays are being experienced during design due to scope verification that was required. The project is forecasted to be delayed by two months.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Cooper City High School

### SMART Facilities Update by Project Cont.

#### Weight Room

Phase: **100% Complete**

#### SCHEDULE: (Calendar Year)

	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2017	Q4 2017	Q4 2017	Q2 2018	Q2 2018	Q3 2018
Actual/Forecast	1/2/2018	1/9/2018	2/5/2018	6/26/2018	7/25/2018	11/1/2018

#### SCOPE:

Weight Room Renovation

#### BUDGET:

\$121,000

#### FLAG:

#### COMMENTS:

#### School Choice Enhancements\*

Phase: **75% Complete**

#### SCHEDULE:

	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2018	TBD	TBD
Actual	11/2018		

#### SCOPE:

School Choice Enhancement

#### BUDGET:

\$100,000

#### FLAG:

#### COMMENTS:

Planned date for Implementation phase shown as TBD will be provided after voting process has been completed by the school community.

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Coral Cove Elementary School

5100 SW 148 AVENUE, MIRAMAR 33027

Location Num	2011
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$698,000
Total Facilities Budget	\$248,000


**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.  
- All dates are based on calendar year. SMART funded projects are included. Only  
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Complete

Primary Renovation: Test and Balance services is completed by a licensed contractor without standard design services. Test and Balance report submitted. Final repairs are pending prior to completion of the project.

School Choice Enhancements: COMPLETED 01/2017. Voting completed 10/12/16. (46) LCD projectors delivered and ceiling mounted. Projects complete 1/25/17.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **90% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2017	N/A	N/A	Q2 2019	Q4 2019	Q1 2020
New Planned	Q4 2017	N/A	N/A	Q2 2019	Q4 2019	Q1 2020
Actual/Forecast	5/1/2017	N/A	N/A	1/10/2018	4/27/2018	7/1/2019
SCOPE:	HVAC Improvements		BUDGET:	FLAG:		
			\$148,000	COMMENTS:		

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q4 2016	Q1 2017
Actual	11/2015	10/2016	01/2017
SCOPE:	School Choice Enhancement		BUDGET:
			\$100,000
FLAG:	COMMENTS:		

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Coral Glades High School

2700 SPORTSPLEX DRIVE, CORAL SPRINGS 33065

Location Num	3861
Board District	4
Board Member	Lori Alhadeff
ADEFP Budget*	\$3,621,000
Total Facilities Budget	\$2,587,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Design**

Primary Renovation: 100% Construction Documents in the permitting process. Building Department is currently reviewing the second submission.

School Choice Enhancements: Voting authorized 9/19/2019. Voting complete 10/15/2019. Coordinating proposals. (2) Laptop Carts, (50) Laptop 300e, (60) cart cable management, Media Center Furniture on order.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **96% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q4 2018	Q3 2019	Q1 2020	Q3 2020
New Planned	Q1 2018	Q2 2018	Q4 2018	Q4 2019	Q3 2020	Q4 2021
Actual/Forecast	8/1/2017	10/6/2017	3/28/2018	Q2 2020		

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG: S - Project Delayed</b>
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,941,000	<b>COMMENTS:</b> Reason: Clarification regarding a new fire alarm panel vs. a new fire alarm system has caused delays to the LOR delivery date. Remedy: The construction documents have been submitted for permit review.
Fire Alarm	\$50,000	
HVAC Improvements	\$375,000	

#### Weight Room

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2017	Q4 2017	Q4 2017	Q2 2018	Q2 2018	Q3 2018
Actual/Forecast	12/19/2017	1/5/2018	2/5/2018	4/5/2018	4/25/2018	7/25/2018

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
Weight Room Renovation	\$121,000	<b>COMMENTS:</b>

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.



## Coral Glades High School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **15%** Complete

SCHEDULE:	PH:1 Planning/Design		PH:2 Implement		PH:3 Complete	
	Planned	Q4 2018	Q4 2019	TBD	TBD	
	Actual	11/2018	10/2019			
SCOPE:	BUDGET:		FLAG:			
School Choice Enhancement	\$100,000		<div>COMMENTS:</div> <div>Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.</div>			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Coral Park Elementary School

8401 WESTVIEW DRIVE, CORAL SPRINGS 33067

Location Num	3041
Board District	4
Board Member	Lori Alhadeff
ADEFP Budget*	\$5,660,621
Total Facilities Budget	\$1,781,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. Building Department currently reviewing the second submission.

School Choice Enhancements: Voting completed 6/1/16. Classroom chairs delivered 01/2017. Coral Park repurposed the allocated funds for the marquee to enhance security on campus. Storefront and electric strike: permit issued; work completed 07/2018. Wind screen for the playground delivered 09/2018. New K-2 and 3-5 playground structure permitted 8/2019; pre-construction meeting held 9/25/2019; construction completed 12/2019.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **97% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2017	Q4 2017	Q2 2018	Q4 2018	Q2 2019	Q1 2020
New Planned	Q3 2017	Q4 2017	Q2 2018	Q4 2019	Q2 2020	Q2 2021
Actual/Forecast	5/1/2017	7/20/2017	2/6/2018	Q2 2020		

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

Health & Safety/Fire Sprinkler Protection Exterior

#### BUDGET:

\$266,000

\$1,415,000

#### FLAG: S - Project Delayed

#### COMMENTS:

Reason: Delays have occurred during the design process. The design firm didn't submit the 90% and 100% submittals within the time frame per the professional service agreement. Remedy: The owner will be enforcing the terms of the contract for delays.

## Coral Park Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **85% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q1 2015	Q2 2016	TBD	TBD
Actual	11/2015	06/2016		

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
School Choice Enhancement	\$100,000	<b>COMMENTS:</b> The school's decision to repurposed the allocated funds for the marquee to enhance security on campus has further impacted the schedule. Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Coral Springs High School

7201 W SAMPLE ROAD, CORAL SPRINGS 33065

Location Num	1151
Board District	4
Board Member	Lori Alhadeff
ADEFP Budget*	\$12,090,000
Total Facilities Budget	\$10,852,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Bid advertisement took place in March 2020.

School Choice Enhancements: COMPLETED 10/2016. Voting completed 6/2/16. ThinkPad's, earth walk carts, printers delivered 07/2016. Projectors received.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **15% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2015	Q1 2016	Q3 2016	Q1 2018	Q2 2018	Q4 2019
New Planned	Q4 2015	Q1 2016	Q3 2016	Q2 2019	Q4 2019	Q4 2021
Actual/Forecast	11/30/2015	2/9/2016	9/23/2016	2/11/2020	Q3 2020	

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$3,396,000
Electrical Improvements	\$458,000
Fire Sprinklers	\$7,000
HVAC Improvements	\$5,029,000
Media Center improvements	\$598,000
STEM Lab improvements	\$1,143,000

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays occurred in the permitting process of the design phase. The design firm took an above average amount of time to complete each submission for the Building Department on multiple occasions. Remedy: The owner will be enforcing terms of the contract for delays and multiple resubmissions. Letter of Recommendation to Permit has been received and contractor procurement is in progress.

#### Weight Room

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q3 2017	Q1 2018	Q2 2018	Q3 2018
Actual/Forecast	4/14/2017	4/21/2017	7/13/2017	1/8/2018	7/25/2018	11/1/2018

SCOPE:	BUDGET:
Weight Room Renovation	\$121,000

**FLAG:**

#### COMMENTS:

**FLAG KEY: S=Schedule B= Budget**

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Coral Springs High School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete	
Planned	Q1 2016	Q2 2016	Q4 2016	Q4 2016
Actual	01/2016	06/2016	10/2016	10/2016
SCOPE:				
School Choice Enhancement				
BUDGET:				
\$100,000				
FLAG:				
COMMENTS:				

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Coral Springs Middle School

10300 W WILES ROAD, CORAL SPRINGS 33076

Location Num	2561
Board District	4
Board Member	Lori Alhadeff
ADEFP Budget*	\$12,886,223
Total Facilities Budget	\$10,602,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. Design firm currently addressing Building Department review comments in order to submit for a second time to permit application.

School Choice Enhancements: Voting authorized 2/16/18. - Voting completed 6/11/18 - (3) Recordex delivered and installed 09/2018. (72) student Laptops, adaptors and (6) Carts delivered 11/2018. Aiphone at the main entrance installed 12/2018. Golf cart delivered 02/2019. Marquee permit issued 6/2019; pre-construction meeting held 10/17/2019; construction start date TBD.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2017	Q4 2017	Q2 2018	Q1 2019	Q3 2019	Q1 2021
New Planned	Q3 2017	Q4 2017	Q2 2018	Q4 2019	Q1 2020	Q4 2021
Actual/Forecast	5/1/2017	7/18/2017	1/30/2018	Q2 2020		

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$2,369,000
HVAC Improvements	\$7,299,000
Media Center improvements	\$640,000

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred during the design phase. A delay was experienced due to required decisions by the District for the fire sprinkler scope of work. Additional delays took place due to multiple backcheck reviews prior to submitting for permit review. Remedy: All activities related to delays have been overcome and the project is

#### HVAC Improvements

Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	N/A	N/A

SCOPE:	BUDGET:
HVAC Improvements - Chiller Replacement	\$194,000

**FLAG:**

#### COMMENTS:

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.


**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Coral Springs Middle School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

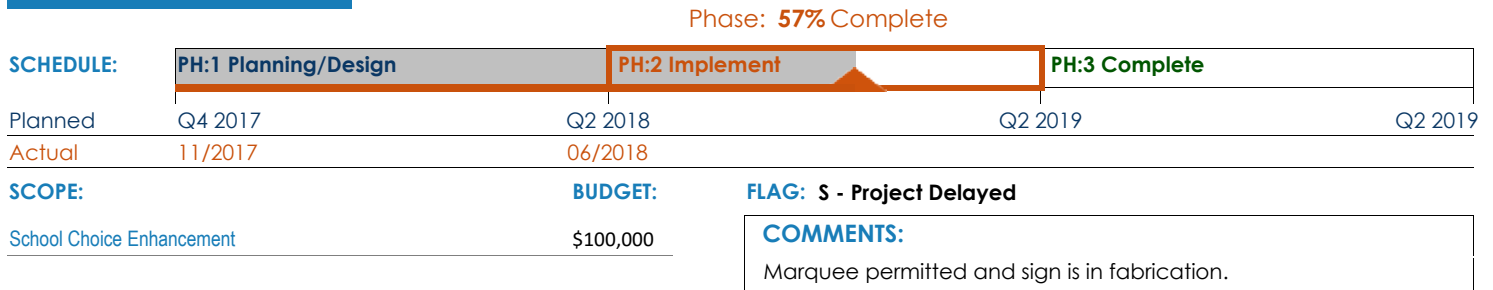

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Coral Springs Pre K-8

(f.k.a. Coral Springs Elementary)

3601 NW 110 AVENUE, CORAL SPRINGS 33065

Location Num	2551
Board District	4
Board Member	Lori Alhadeff
ADEFP Budget*	\$4,627,262
Total Facilities Budget	\$2,638,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. Design firm currently addressing Building Department comments prior to submitting the second time for permit application.

School Choice Enhancements: Principal's letter initiated 11/30/2018 for Year 5 group. Kick-off meeting is being scheduled.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **96% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q1 2019	Q3 2019	Q1 2020	Q3 2020
New Planned	Q1 2018	Q2 2018	Q1 2019	Q1 2020	Q3 2020	Q3 2021
Actual/Forecast	11/13/2017	12/19/2017	7/9/2018	Q3 2020		

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

HVAC Improvements

Media Center improvements

#### BUDGET:

\$190,000

\$2,039,000

\$184,000

#### FLAG: S - Project Delayed

#### COMMENTS:

Delays have occurred during the backcheck review of the Construction Documents prior to submitting for permit review. Multiple submissions were required in order to close out comments made by the review team. The project is currently delayed by 4 months. It is anticipated these delays could extend if the design requires multiple submissions to the Building Department to receive a Letter of Recommendation to Permit.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Coral Springs Pre-K - 8

(f.k.a. Coral Springs Elementary)

### SMART Facilities Update by Project Cont.

#### HVAC Improvements

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	10/1/2016	12/1/2016 8/28/2017

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
HVAC Improvements - Chiller Replacement	\$125,000	<b>COMMENTS:</b>

#### School Choice Enhancements\*

Phase: **10% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2018	TBD	TBD
Actual	11/2018		

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
School Choice Enhancement	\$100,000	<b>COMMENTS:</b>

Planned date for Implementation phase shown as TBD will be provided after voting process has been completed by the school community.

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Country Hills Elementary School

10550 WESTVIEW DRIVE, CORAL SPRINGS 33076

Location Num	3111
Board District	4
Board Member	Lori Alhadeff
ADEFP Budget*	\$5,148,310
Total Facilities Budget	\$4,513,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. Design firm currently addressing Building Department comments prior to submitting the fourth time for permit application.

School Choice Enhancements: Voting authorized 5/28/2019. Voting completed 6/10/2019 - P-number requested. Aiphone at the main entrance, table for the additional kindergarten section, two-way radios on order. (15) Motorola two-way radios delivered 11/2019. (10) Radio Batteries, Tables for the additional Kidergarten section delivered 01/2020.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **97% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2017	Q1 2018	Q4 2018	Q2 2019	Q4 2019	Q3 2020
New Planned	Q4 2017	Q1 2018	Q4 2018	Q1 2020	Q3 2020	Q1 2022
Actual/Forecast	7/1/2017	9/20/2017	5/3/2018	Q4 2020		

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

Fire Sprinklers

HVAC Improvements

#### BUDGET:

\$1,696,000

\$120,000

\$2,597,000

#### FLAG: S - Project Delayed

#### COMMENTS:

Reason: Delays have occurred during the design phase. The design firm has not met the deadlines of the design deliverables. Remedy: The owner will be enforcing terms of the contract for delays.

FLAG KEY: S=Schedule B= Budget

S-Project Delayed=Schedule: Project has missed the planned milestone date for progressing to the next phase in the process.

S-Delay Possible=Schedule: Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

B=Budget: reflects a need for board approved increase in funding based on bid and/or change order results.

## Country Hills Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **10% Complete**

SCHEDULE:	PH:1 Planning/Design		PH:2 Implement		PH:3 Complete	
	Planned	Q4 2018	Q2 2019	TBD	TBD	
Actual	11/2018		06/2019			
SCOPE:		BUDGET:		FLAG:		
School Choice Enhancement		\$100,000		<b>COMMENTS:</b>  Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.		

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Country Isles Elementary School

2300 COUNTRY ISLES ROAD, WESTON 33326

Location Num	2981
Board District	6
Board Member	Laurie Rich Levinson
ADEFP Budget*	\$1,759,660
Total Facilities Budget	\$1,339,660

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Notice to Proceed with construction is being executed.

School Choice Enhancements:

COMPLETED 12/2016 - Sand replacement with PIP surfacing in K-2 and 3-5 play areas.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **80% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q1 2018	Q3 2018	Q1 2019	Q1 2020
New Planned	Q2 2017	Q2 2017	Q1 2018	Q3 2019	Q1 2020	Q1 2021
Actual/Forecast	4/1/2017	6/22/2017	1/18/2018	3/29/2019	Q2 2020	

#### SCOPE:

Additional Funding - Board Approved 01/14/20 (JJ-3)

Fire Alarm

HVAC Improvements

Media Center improvements

#### BUDGET:

\$681,660

\$294,000

\$104,000

\$160,000

#### FLAG: SB - Project Delayed

#### COMMENTS:

Reason: Delays have occurred during bid and award due to contractor preparation of documentation for execution of the Notice to Proceed. Remedy: Notice to Proceed is scheduled for April 2020. Budget: Additional funding of \$681,660 was approved by the Board on 1/14/2020 in conjunction with the approval to award the construction agreement for the project to the CSMP contractor.

FLAG KEY: S=Schedule B= Budget

S-Project Delayed=Schedule: Project has missed the planned milestone date for progressing to the next phase in the process.

S-Delay Possible=Schedule: Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

B=Budget: reflects a need for board approved increase in funding based on bid and/or change order results.

## Country Isles Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **100%** Complete

SCHEDULE:	PH:1 Planning/Design		PH:2 Implement		PH:3 Complete	
Planned	Q1 2015		Q1 2016		Q1 2017	
Actual	11/2015		02/2016		12/2016	
SCOPE:		BUDGET:		FLAG:		
School Choice Enhancement		\$100,000		COMMENTS:		

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Cresthaven Elementary School

801 NE 25 STREET, POMPANO BEACH 33064

Location Num	0901
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$4,862,123
Total Facilities Budget	\$4,516,123

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


### PRIMARY PROJECTS CURRENT STATUS: Hire Design Team

Primary Renovation: Authorization to Proceed is on hold pending the hiring of the CMAR contractor.

School Choice Enhancements:

Principal's letter initiated 11/30/2018 for Year 5 group. Kick-off meeting has been held. Ballot development is in progress.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2018	Q3 2018	Q4 2018	Q2 2019	Q3 2019	Q4 2020
New Planned	Q3 2018	Q3 2018	Q2 2019	Q4 2020	Q3 2021	Q4 2022
Actual/Forecast	9/28/2017	6/27/2018	Q2 2020			

SCOPE:	BUDGET:
ADA Restrooms	\$592,123
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,193,000
HVAC Improvements	\$2,631,000

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays occurred due to additional review of the delivery method and Board approval to perform the project using CMAR services. Remedy: Board approval of the CM firm is pending. Once the CMAR firm has been hired, an Authorization to Proceed will be executed for both design firm and CMAR contractor.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.



## Cresthaven Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **10% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q4 2018	TBD	TBD	TBD
Actual	11/2018			

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
School Choice Enhancement	\$100,000	<b>COMMENTS:</b> Planned date for Implementation phase shown as TBD will be provided after voting process has been completed by the school community.

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Croissant Park Elementary School

1800 SW 4 AVENUE, FORT LAUDERDALE 33315

Location Num	0221
Board District	3
Board Member	Heather P. Brinkworth
ADEFP Budget*	\$4,123,000
Total Facilities Budget	\$3,761,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. All discipline reviews have been approved and the Letter of Recommendation to Permit is pending.

School Choice Enhancements: Voting completed 6/3/2019 - Facilities equipment delivered 09/2019. (1) Blower, (1) Pressure Cleaner and (1) Surface Cleaner delivered 12/2019. (3) Vacuums, digital marquee on order.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **98% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2017	Q1 2018	Q4 2018	Q2 2019	Q1 2020	Q3 2020
New Planned	Q4 2017	Q1 2018	Q4 2018	Q1 2020	Q3 2020	Q1 2022
Actual/Forecast	8/1/2017	10/6/2017	3/28/2018	Q2 2020		

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$851,000
Fire Alarm	\$294,000
Fire Sprinklers	\$812,000
HVAC Improvements	\$1,704,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred during the design phase. The design firm has required additional time to address all review comments during permitting. Remedy: All discipline reviews have been approved and the Letter of Recommendation to permit is pending.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Croissant Park Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **10% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q4 2018	Q2 2019	TBD	TBD
Actual	11/2018	06/2019		
<b>SCOPE:</b>	<b>BUDGET:</b>		<b>FLAG:</b>	
School Choice Enhancement	\$100,000		<b>COMMENTS:</b> Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Cross Creek School

1010 NW 31ST AVENUE, POMPANO BEACH 33069

Location Num	3222
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$1,500,000
Total Facilities Budget	\$1,360,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Hire Contractor**

Primary Renovation: Contractor procurement in progress. Pending new CSMP contractor list for procurement.

School Choice Enhancements: Kick-off meeting scheduled for 4/3/2019; ballot development in progress.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **10% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2017	Q1 2018	Q4 2018	Q2 2019	Q1 2020	Q3 2020
New Planned	Q4 2017	Q1 2018	Q4 2018	Q4 2019	Q1 2020	Q1 2021
Actual/Forecast	8/1/2017	10/6/2017	5/3/2018	1/7/2020	Q3 2020	Q3 2020

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

Fire Alarm

HVAC Improvements

#### BUDGET:

\$405,000

\$420,000

\$435,000

#### FLAG: S - Project Delayed

#### COMMENTS:

Reason: Delays have occurred throughout the design process.  
Remedy: All discipline reviews have been approved by the Building Department. The current CSMP contract has expired. The project will experience additional delays until the new CSMP contractor list is approved.

FLAG KEY: S=Schedule B= Budget

S-Project Delayed=Schedule: Project has missed the planned milestone date for progressing to the next phase in the process.

S-Delay Possible=Schedule: Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

B=Budget: reflects a need for board approved increase in funding based on bid and/or change order results.

## Cross Creek School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **25%** Complete

<b>SCHEDULE:</b>	<b>PH:1 Planning/Design</b>	<b>PH:2 Implement</b>	<b>PH:3 Complete</b>
Planned	Q4 2018	TBD	TBD
Actual	11/2018		

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
School Choice Enhancement	\$100,000	<b>COMMENTS:</b> Planned date for Implementation phase shown as TBD will be provided after voting process has been completed by the school community.

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Crystal Lake Middle School

3551 NE 3 AVENUE, POMPANO BEACH 33064

Location Num	1871
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$2,760,525
Total Facilities Budget	\$2,335,525

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. Design firm currently addressing Building Department comments prior to submitting the fourth time for permit application.

School Choice Enhancements: Ballot approved for voting. Voting authorized 5/3/2019. Voting completed 02/2020. (70) Cafeteria Tables on order. Coordinating additional proposals.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **98% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q1 2019	Q3 2019	Q1 2020	Q3 2020
New Planned	Q1 2018	Q2 2018	Q1 2019	Q1 2020	Q2 2020	Q2 2021
Actual/Forecast	11/13/2017	12/19/2017	8/20/2018	Q2 2020		

#### SCOPE:

Art Room Renovation and Equipment	\$85,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$812,000
Conversion of Existing Space to Music and/or Art Lab(s)	\$284,000
HVAC Improvements	\$244,000
Install Fire Alarm	\$472,525
Media Center improvements	\$338,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays occurred during the design phase. The design firm has taken an above average amount of time to resubmit plans for permit review. The design firm took four months to resubmit the second time for review, and three months to resubmit the third time for review. Remedy: The owner will be enforcing terms of the

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Crystal Lake Middle School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **10% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q4 2018	Q1 2020	TBD	TBD
Actual	11/2018	02/2020		
<b>SCOPE:</b>	<b>BUDGET:</b>		<b>FLAG:</b>	
School Choice Enhancement	\$100,000		<b>COMMENTS:</b> Planned date for Implementation phase shown as TBD will be provided after voting process has been completed by the school community.	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Cypress Bay High School

18600 VISTA PARK BOULEVARD, WESTON 33332

Location Num	3623
Board District	6
Board Member	Laurie Rich Levinson
ADEFP Budget*	\$35,428,323
Total Facilities Budget	\$33,144,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


### PRIMARY PROJECTS CURRENT STATUS: Construction

Primary Renovation: Construction is in progress. Air handling units have been replaced. Condensing unit replacement is in progress. Minor delays in the replacement of Condensing Unit, CU-9 continue. Roofing base sheet was completed with fabrication of metal trim in progress.

Classroom Addition: Construction in progress. First floor rough-ins are in progress. Second floor slab is being poured with third floor deck in progress. Stair work is in progress.

School Choice Enhancements: COMPLETED 02/2017. Voting completed 5/26/2017. Projectors delivered 08/2016. (112) Printers delivered 07/2016. Projector in auditorium installed 09/2016. (4) Recordex delivered and installed 11/2016. Office furniture delivered 02/2017.

### SMART Facilities Update By Project



#### Primary Renovation

	Phase: <b>90% Complete</b>					
<b>SCHEDULE:</b> (Calendar Year)	<b>1: Planning</b>	<b>2: Hire A/E</b>	<b>3: Design</b>	<b>4: Hire Contractor</b>	<b>5: Construction</b>	<b>6: Closeout</b>
Planned	Q2 2016	Q3 2016	Q1 2017	Q1 2018	Q3 2018	Q4 2019
Actual/Forecast	6/27/2016	8/2/2016	2/22/2017	9/25/2018	3/21/2019	8/14/2020

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$652,000
HVAC Improvements	\$580,000
Safety / Security Upgrade	\$107,000

#### BUDGET:

#### FLAG: S - Project Delayed

#### COMMENTS:

Original contractual date of substantial completion is 12/26/2019. Reason: Delays were experienced in construction related to roof mounting of HVAC equipment. Remedy: Pending decision of the roof stand prior to completion of the roofing work and HVAC stand installation. Substantial completion is scheduled for Q3 2020. Minor delay in finishing the roofing work in order to receive Substantial Completion.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Cypress Bay High School

### SMART Facilities Update by Project Cont.

#### Classroom Addition

Phase: **35% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2016	Q3 2016	Q1 2017	Q4 2018	Q1 2019	Q2 2020
Actual/Forecast	6/27/2016	8/2/2016	2/22/2017	3/8/2019	6/27/2019	12/6/2020

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG: S - Delay Possible</b>
Additional Funding - Board Approved 06/11/19 (JJ-11)	\$18,839,000	<b>COMMENTS:</b> Original contractual date of substantial completion is 12/6/2020. Project is currently on pace. Delays were experienced during the design phase that were not recovered in bid and award or construction. Multiple backcheck reviews were required to closeout comments before the design firm submitted for permit review.
CR Addition - Prep Work	\$0	
CR Addition to allow for removal of portable buildings	\$12,400,000	

#### Weight Room

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q3 2017	Q3 2017	Q3 2017	Q4 2017
Actual/Forecast	4/14/2017	4/21/2017	7/13/2017	8/1/2017	10/19/2017	12/17/2017

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
Weight Room Renovation	\$121,000	<b>COMMENTS:</b>

#### Track

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	Q1 2017	Q2 2017	Q4 2017	Q1 2018
Actual/Forecast	8/22/2017	8/29/2017	8/30/2017	10/14/2017	10/22/2017	3/30/2018

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
Track Resurfacing	\$345,000	<b>COMMENTS:</b>

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2016	Q2 2016	Q1 2017
Actual	01/2016	05/2016	02/2017

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
School Choice Enhancement	\$100,000	<b>COMMENTS:</b>

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Cypress Elementary School

851 SW 3 AVENUE, POMPANO BEACH 33060

Location Num	1781
Board District	3
Board Member	Heather P. Brinkworth
ADEFP Budget*	\$4,311,982
Total Facilities Budget	\$3,857,982

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Complete

Primary Renovation: Construction in substantial completion. Final inspections are pending.

School Choice Enhancements: Completed - Voting completed 5/17/2016. Picnic tables delivered 7/2016. Furniture for student service area, teacher workroom renovation delivered and installed 9/2016. PIP project completed 12/2016. Marquee PO canceled for Robson Corporation; District is no longer using this vendor due to lack of performance. Marquee permitted 9/12/2019; pre-construction meeting held 10/22/2019; installation in progress 12/16/2019.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **10% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2015	Q4 2015	Q3 2016	Q1 2017	Q3 2017	Q2 2018
New Planned	Q4 2015	Q4 2015	Q3 2016	Q1 2017	Q3 2017	Q1 2019
Actual/Forecast	10/19/2015	12/8/2015	8/31/2016	5/8/2017	2/21/2018	3/3/2020

#### SCOPE:

Additional Funding - Board Approved 12/19/17 (JJ-15)	\$452,897
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$637,564
Fire Sprinklers	\$634,000
Media Center improvements	\$177,000
Replace existing unit ventilators (appr. 42) with new unit ventilators, duct and diffusers.	\$1,747,603
Safety / Security Upgrade	\$103,000

#### BUDGET:

#### FLAG:

#### COMMENTS:

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Cypress Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **100% Complete**

SCHEDULE:				
	PH:1 Planning/Design		PH:2 Implement	
	PH:3 Complete			
Planned	Q1 2015	Q2 2016	Q1 2018	Q1 2018
Actual	11/2015	05/2016	01/2020	01/2020
SCOPE:		BUDGET:	FLAG:	
Additional Funding - Board Approved 04/23/19 (JJ-14)		\$5,918	COMMENTS:	
School Choice Enhancement		\$100,000		

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.

COMPLETED



## Cypress Run Education Center

2800 NW 30TH AVENUE, POMPANO BEACH 33069

Location Num	2123
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$248,000
Total Facilities Budget	\$177,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.


- All dates are based on calendar year. SMART funded projects are included. Only  
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Complete**

Primary Renovation: Complete - Test and Balance services is completed by a licensed contractor without standard design services.

School Choice Enhancements: COMPLETED 01/2017. Voting completed 5/16/16. Staff and student laptops - Computers for other areas such as computer lab, TV production, laptops and USB drives delivered 01/2017.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout	
Planned	Q1 2017	N/A	N/A	Q3 2018	Q1 2019	Q2 2019	Q3 2019
New Planned	Q1 2017	N/A	N/A	Q3 2018	Q1 2019	Q2 2019	Q3 2019
Actual/Forecast	11/3/2016	N/A	N/A	1/10/2018	4/10/2018	6/19/2019	8/28/2019
SCOPE:	HVAC Improvements		BUDGET:	FLAG: <div>COMMENTS:</div>			
			\$77,000				

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q2 2016	Q1 2017
Actual	11/2015	05/2016	01/2017
SCOPE:	School Choice Enhancement		BUDGET:
		\$100,000	FLAG:
			COMMENTS:

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Dania Elementary School

300 SE 2 AVENUE, DANIA 33004

Location Num	0101
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$2,861,000
Total Facilities Budget	\$2,602,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: Scope revisions are in progress. 50% Construction Documents are in progress with revised scope. Presentation of the scope revisions was on 12/11/2019. Design of the scope revisions is currently taking place with presentation of the revised design scheduled for Board workshop on 4/14/2020.

School Choice Enhancements:

Principal's letter initiated 11/30/2018 for Year 5 group. Kick-off meeting has been held. Ballot development is in progress.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **55% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q1 2019	Q3 2019	Q1 2020	Q2 2020
New Planned	Q1 2018	Q2 2018	Q1 2019	Q4 2019	Q3 2020	Q1 2022
Actual/Forecast	7/1/2017	9/20/2017	5/4/2018	Q2 2021		

SCOPE:	BUDGET:
Art Room Renovation and Equipment	\$65,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$266,000
Electrical Improvements	\$610,000
Improvements to or Replacement of building 2	\$1,065,000
Media Center improvements	\$213,000
Music Room Renovation	\$136,000
Safety / Security Upgrade	\$147,000

**FLAG: S - Project Delayed**

#### COMMENTS:

The design process is now forecasted for completion in Q2 2021 due to the revision in scope related to right sizing Building 2. The project design schedule is being closely monitored due to the delays in scope revisions.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.



## Dania Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **25%** Complete

<b>SCHEDULE:</b>	<b>PH:1 Planning/Design</b>	<b>PH:2 Implement</b>	<b>PH:3 Complete</b>
Planned	Q4 2018	TBD	TBD
Actual	11/2018		

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
School Choice Enhancement	\$100,000	<b>COMMENTS:</b> Planned date for Implementation phase shown as TBD will be provided after voting process has been completed by the school community.

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Dave Thomas Education Center - East

180 SW 2ND STREET, POMPANO BEACH 33060

Location Num	3651
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$2,876,494
Total Facilities Budget	\$2,719,494


**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.  
- All dates are based on calendar year. SMART funded projects are included. Only  
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction is in progress. Concrete pads for exterior HVAC units have been installed. Units have been delivered and are pending installation. The roofing sub-permit binder has been submitted for review.

School Choice Enhancements: COMPLETED 06/2018. Voting completed 6/2/17. Lenovo laptops delivered 08/2017. Marquee installed, electrical tie-in completed 02/2018. Front office furniture delivered 05/2018.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **10% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q1 2018	Q3 2018	Q1 2019	Q4 2019
New Planned	Q2 2017	Q2 2017	Q1 2018	Q1 2019	Q3 2019	Q3 2020
Actual/Forecast	4/6/2017	4/19/2017	11/17/2017	2/27/2019	9/6/2019	9/27/2020

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
Additional Funding - Board Approved 07/23/19 (JJ-3)	\$1,861,494	<b>COMMENTS:</b> Original contractual date of substantial completion is 9/27/2020. Project is currently on pace.
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$373,000	
HVAC Improvements	\$385,000	

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2016	Q2 2017	Q1 2018
Actual	01/2016	06/2017	06/2018

<b>SCOPE:</b>	<b>BUDGET:</b>	<b>FLAG:</b>
School Choice Enhancement	\$100,000	<b>COMMENTS:</b>

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Dave Thomas Education Center - West

4690 COCONUT CREEK PARKWAY, COCONUT CREEK 33066

Location Num	2031
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$212,000
Total Facilities Budget	\$100,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.


- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **N/A**

School Choice Enhancements: COMPLETED 12/2017 - Voting completed 10/11/16. Reconstructing of Room 202 is completed. Technology items and outdoor furniture delivered and installed 02/2017. Recordex delivered 03/2017. Wall wraps delivered 12/2017.

### SMART Facilities Update By Project



#### School Choice Enhancements\*

<b>SCHEDULE:</b>		<b>PH:1 Planning/Design</b>		<b>PH:2 Implement</b>	<b>PH:3 Complete</b>	Phase:100% Complete
Planned	Q1 2015		Q4 2016		Q4 2017	Q4 2017
Actual	11/2015		10/2016		12/2017	12/2017
<b>SCOPE:</b>		<b>BUDGET:</b>		<b>FLAG:</b>		
School Choice Enhancement		\$100,000		<b>COMMENTS:</b>		

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Davie Elementary School

7025 SW 39 STREET, DAVIE 33314

Location Num	2801
Board District	6
Board Member	Laurie Rich Levinson
ADEFP Budget*	\$5,536,700
Total Facilities Budget	\$5,196,700

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Board approval of the contractor and additional funding took place in March 2020. Pending execution of the Notice to Proceed.

School Choice Enhancements:

COMPLETED 02/2020 - Voting authorized 2/21/2018 - Voting completed 3/30/18 - (50) Laptops, (25) Desktops, (2) Earthwalk carts, (8) Printers, Reading tables, Cafeteria system upgrades, stage curtains, teacher lounge upgrade, classroom rugs, and (3) Recordex delivered and installed 09/2018. Teacher lounge updates - (Conference table, cabinets, presentation board, 2 leather seating, 6 black leather chairs, 5 leather fabric) delivered 06/2019. (4) iPads delivered 10/2019. (6) HDMI cables delivered 02/2020.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **70% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2016	Q1 2017	Q4 2017	Q2 2018	Q4 2018	Q4 2019
New Planned	Q4 2016	Q1 2017	Q4 2017	Q2 2019	Q3 2019	Q4 2020
Actual/Forecast	11/18/2016	3/13/2017	8/28/2017	4/11/2019	Q2 2020	

#### SCOPE:

Additional Funding - Board Approved 03/03/20 (JJ-2)	\$2,220,700
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,074,000
Fire Sprinklers	\$685,000
HVAC Improvements	\$809,000
Media Center improvements	\$235,000
Safety / Security Upgrade	\$73,000

#### BUDGET:

**FLAG: SB - Project Delayed**

#### COMMENTS:

Reason: The project was delayed three quarters due to the required roofing reality check. Remedy: Notice to Proceed is being executed. Budget: Additional funding of \$2,220,700 was approved by the Board on 3/3/2020 in conjunction with the approval to award the construction agreement for the project.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Davie Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:				
PH:1 Planning/Design		PH:2 Implement		PH:3 Complete
Planned	Q4 2016	Q1 2018	Q1 2020	Q1 2020
Actual	12/2016	03/2018	02/2020	02/2020
SCOPE:		BUDGET:	FLAG:	
School Choice Enhancement		\$100,000	COMMENTS:	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Deerfield Beach Elementary School

650 NE 1 STREET, DEERFIELD BEACH 33441

Location Num	0011
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$6,675,445
Total Facilities Budget	\$6,333,445

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Bid opening has occurred. Pending Board award.

School Choice Enhancements: Voting completed 3/21/17. Fence around the butterfly garden installed, Tables and Stools delivered on 11/2018. (2) bookcases on order. Outdoor Classroom permitted on 05/2018 - plan change approved 12/2018; construction began 1/14/2019; construction completed 03/2019. (15) 8x12 classroom rugs, (301) chairs on order.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **55% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2016	Q4 2016	Q3 2017	Q2 2018	Q4 2018	Q4 2019
New Planned	Q3 2016	Q4 2016	Q3 2017	Q1 2019	Q3 2019	Q4 2020
Actual/Forecast	9/12/2016	10/18/2016	5/12/2017	2/6/2019	Q2 2020	Q1 2020

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$369,000
Fire Alarm	\$294,000
Fire Sprinklers	\$725,000
HVAC Improvements	\$529,000
Lead Base Paint Abatement	\$326,445
Media Center improvements	\$378,000
Renovations to Building 1 (Historic)	\$2,862,000
Replacement of wood windows at Building #1 - Auditorium.	\$750,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred in the Bid and Award phase. The window replacement and lead based paint abatement is being included in the bid documents. The project was delayed twice during the bid advertisement due to advertisement extension caused by necessary responses to RFI's that would ensure the

## Deerfield Beach Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **92% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q1 2015	Q1 2017	TBD	TBD
Actual	11/2015	03/2017		
<b>SCOPE:</b>	<b>BUDGET:</b>		<b>FLAG:</b>	
School Choice Enhancement	\$100,000		<b>COMMENTS:</b> Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Deerfield Beach High School

910 SW 15 STREET, DEERFIELD BEACH 33441

Location Num	1711
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$13,950,000
Total Facilities Budget	\$12,907,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor


Primary Renovation - Phase 1: Contractor procurement in progress. Pending scope confirmation involving ultrasound testing performed on existing chilled water piping to determine potential cost savings in construction. Bid advertisement is scheduled for April 2020.

Primary Renovation - Phase 2: Authorization to Proceed is on hold pending the hiring of the CMAR contractor.

School Choice Enhancements:

Kick-off meeting held 12/6/2019. Ballot reviewed, in compliance 4/29/2019. Voting results received 9/19/2019. Aiphone at the Single Point of Entry, (2) Gym scoreboards, Gator on order. NTP for installation of scoreboards in progress.

### SMART Facilities Update By Project



#### Primary Renovation - Phase 1

Phase: **5% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2015	Q1 2016	Q4 2016	Q2 2017	Q4 2017	Q1 2019
New Planned	Q4 2015	Q1 2016	Q4 2016	Q1 2019	Q2 2019	Q4 2020
Actual/Forecast	11/5/2015	1/20/2016	10/19/2016	1/8/2020	Q3 2020	Q1 2021

#### SCOPE:

Fire Sprinklers

Roof Repairs and HVAC

#### BUDGET:

\$22,000

\$8,617,899

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred during the permitting process. The design firm was non-responsive after the second submission was reviewed and the Building Department provided comments. Remedy: The Letter of Recommendation to Permit has been received. Pending final testing of existing piping prior to advertising



## Deerfield Beach High School

### SMART Facilities Update by Project Cont.

#### Primary Renovation - Phase 2

Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q1 2019	Q3 2019	Q1 2020	Q4 2020
New Planned	Q1 2018	Q2 2018	Q2 2019	Q4 2020	Q1 2021	Q3 2022
Actual/Forecast	11/13/2017	12/13/2017	Q2 2020			

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$836,000
Electrical Improvements	\$303,000
Media Center improvements	\$688,000
Safety / Security Upgrade	\$114,000
STEM Lab improvements	\$1,971,000

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays occurred due to additional review of the delivery method and Board approval to perform the project using CMAR services. Remedy: Board approval of the CM firm is pending. Once the CMAR firm has been hired, an Authorization to Proceed will be executed for both design firm and CMAR contractor.

#### Weight Room

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2017	Q4 2017	Q4 2017	Q2 2018	Q2 2018	Q3 2018
Actual/Forecast	12/31/2017	1/17/2018	2/5/2018	5/31/2018	6/1/2018	11/19/2018

SCOPE:	BUDGET:
Weight Room Renovation	\$121,000

**FLAG:**

#### COMMENTS:

#### Cooling Tower Replacement

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	7/1/2016	8/1/2016

SCOPE:	BUDGET:
Roof Repairs and HVAC - Cooling tower replacement	\$134,101

**FLAG:**

#### COMMENTS:

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Deerfield Beach High School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **10% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q4 2018	Q3 2019	TBD	TBD
Actual	11/2018	09/2019		
<b>SCOPE:</b>	<b>BUDGET:</b>		<b>FLAG:</b>	
School Choice Enhancement	\$100,000		<b>COMMENTS:</b> Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Deerfield Beach Middle School

701 SE 6 AVENUE, DEERFIELD BEACH 33441

Location Num	0911
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$4,757,000
Total Facilities Budget	\$4,433,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Design Team

Primary Renovation: Authorization to Proceed is on hold pending the hiring of the CMAR contractor. Scope Validation has been completed. The project has moved back to Designer Procurement until the new ATP has been executed. The project design will then continue from where it left off.

School Choice Enhancements: Ballot approved for voting; voting authorized 5/22/2019. Voting completed 6/6/2019. Broadcasting equipment delivered 11/2019. (32) High student desks, (46) Armless chairs, (7) table tops, (7) flip down table base, (1) teachers desk and (4) Colison tables for STEM Lab room and more furniture for Room 212 Medical and Rooms 301E - 301F - 302, (4) Zenergy stools, (16) armless chairs delivered 12/2019. (3) Makerbot 3D Printers delivered 03/2020. (4) Pressure Kits, window wraps, Washer and Dryer on order.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q1 2019	Q3 2019	Q2 2020	Q4 2020
New Planned	Q1 2018	Q2 2018	Q2 2019	Q4 2020	Q3 2021	Q4 2022
Actual/Forecast	9/28/2017	6/27/2018	Q2 2020			

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$2,227,000
Fire Alarm	\$461,000
Fire Sprinklers	\$632,000
HVAC Improvements	\$714,000
Media Center improvements	\$299,000

#### BUDGET:

FLAG: **S** - Project Delayed

#### COMMENTS:

Reason: Delays occurred due to additional review of the delivery method and Board approval to perform the project using CMAR services. Remedy: Board approval of the CM firm is pending. Once the CMAR firm has been hired, an Authorization to Proceed will be executed for both design firm and CMAR contractor.

FLAG KEY: **S**=Schedule **B**= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Deerfield Beach Middle School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **85% Complete**

SCHEDULE:	<div><div>PH:1 Planning/Design</div><div>PH:2 Implement</div><div>PH:3 Complete</div></div>			
	Planned	Q4 2018	Q2 2019	TBD
	Actual	11/2018	06/2019	
SCOPE:				
School Choice Enhancement				
BUDGET:				
\$100,000				
FLAG:	<div>COMMENTS:</div> <div>Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.</div>			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Deerfield Park Elementary School

650 SW 3 AVENUE, DEERFIELD BEACH 33441

Location Num	0391
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$5,601,000
Total Facilities Budget	\$5,340,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Bid opening has occurred. Pending Board award of the contractor.

School Choice Enhancements: Voting completed 10/11/2018, Marquee permitted 7/19/2019; pre-construction meeting held 10/17/2019; structural installation began 12/19/2019. Proposals for the TVs and production studio are being coordinated.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **25% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2017	Q4 2017	Q3 2018	Q1 2019	Q4 2019	Q3 2020
New Planned	Q3 2017	Q4 2017	Q3 2018	Q1 2019	Q3 2019	Q3 2020
Actual/Forecast	5/1/2017	7/18/2017	1/8/2018	3/4/2019	Q2 2020	Q4 2020

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,236,000
Fire Alarm	\$293,000
Fire Sprinklers	\$808,000
HVAC Improvements	\$2,893,000
PE/Athletic Improvements	\$10,000

**FLAG: S - Project Delayed**

#### COMMENTS:

Funding Year 1 thru 3 projects are to take priority for advertisement of bid. The project is funded under Year 4 and was advertised after the available funding Year 1 thru 3 projects were advertised.

## Deerfield Park Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **10% Complete**

SCHEDULE:	PH:1 Planning/Design		PH:2 Implement		PH:3 Complete	
	Planned	Q4 2017	Q3 2018	TBD	TBD	
	Actual	11/2017	10/2018			
SCOPE:	BUDGET:		FLAG:			
School Choice Enhancement	\$100,000		<div>COMMENTS:</div> <div>Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.</div>			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Dillard 6-12 School

2501 NW 11 STREET, FORT LAUDERDALE 33311

Location Num	0371
Board District	5
Board Member	Dr. Rosalind Osgood
ADEFP Budget*	\$8,929,232
Total Facilities Budget	\$8,179,232

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


## PRIMARY PROJECTS CURRENT STATUS: Construction

Primary Renovation: Construction in progress. Site lighting installation requires concrete light pole repairs prior to inspection approval. HVAC in Building 8 is in progress. Exit signage installation is complete. Chiller installation at Building 12 is complete with minor details remaining.

School Choice Enhancements:

COMPLETED 03/2020 - Voting completed 9/25/17 - Poster Maker and 3D Printer delivered and training completed 11/2017. Student laptops, and chairs delivered 12/2017. Additional furniture and golf carts delivered 01/2018. Additional chairs delivered 03/2018. Marquee permitted 08/18 and sign is in fabrication. Marquee Pre-construction meeting held 10/9/2018; Art work confirmed by the school 1/31/2019. Marquee installation completed 05/2019.

## SMART Facilities Update By Project



### Primary Renovation

Phase: **36% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2016	Q2 2016	Q4 2016	Q4 2017	Q1 2018	Q1 2019
New Planned	Q1 2016	Q2 2016	Q4 2016	Q1 2019	Q2 2019	Q1 2021
Actual/Forecast	2/24/2016	5/3/2016	12/13/2016	12/21/2018	5/3/2019	11/24/2020

### SCOPE:

Additional Funding - Board Approved 4/23/19 (JJ-2)  
 Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)  
 Electrical Improvements  
 Fire Sprinklers  
 HVAC Improvements  
 Safety / Security Upgrade

### BUDGET:

\$4,266,232  
 \$2,441,000  
 \$522,000  
 \$375,000  
 \$282,000  
 \$72,000

### FLAG:

#### COMMENTS:

Original contractual date of substantial completion is 11/24/2020. Project is currently on pace.



## Dillard 6-12 School

### SMART Facilities Update by Project Cont.

#### Weight Room

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2017	Q1 2017	Q3 2017	Q3 2017	Q3 2017	Q4 2017
Actual/Forecast	3/3/2017	3/10/2017	8/17/2017	8/18/2017	8/23/2017	12/15/2017

<b>SCOPE:</b> Weight Room Renovation	<b>BUDGET:</b> \$121,000	<b>FLAG:</b> <b>COMMENTS:</b>
---	-----------------------------	----------------------------------

#### School Choice Enhancements\*

Phase: **99% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q3 2017	Q1 2020
Actual	11/2015	09/2017	03/2020

<b>SCOPE:</b> School Choice Enhancement	<b>BUDGET:</b> \$100,000	<b>FLAG:</b> <b>COMMENTS:</b> All items approved by voting process have been delivered and installed. School is determining how to spend the remaining contingency portion of the SCEP funding.
--	-----------------------------	---

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



<b>Location Num</b>	0271
<b>Board District</b>	5
<b>Board Member</b>	Dr. Rosalind Osgood
<b>ADEFP Budget*</b>	\$1,900,000
<b>Total Facilities Budget</b>	\$1,777,000

- All dates are based on calendar year. SMART funded projects are included. Only  
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

School Choice Enhancements: Voting completed 6/14/18 - Outdoor mats, classroom rugs, (2) flat screen TVs, Window Wraps and Custodial Equipment delivered and installed 08/2018. (10) Two-way radios delivered 09/2018. Golf Cart accessories and stage curtains installed 10/2018. Media Center Furniture TV and (22) Window wraps delivered 02/2019. Additional window wraps delivered 06/2019. (1) Used Golf Cart delivered 01/2020.

1 **PLANNING**  
Develop & Validate Project Scope

2 **HIRE DESIGN TEAM**  
Advertise and Hire Design Team

3 **DESIGN**  
Prepare Plan Drawings to release to contractor/vendor

4 **HIRE CONTRACTOR**  
Bid and Hire Contractor to Implement Renovations

5 **CONSTRUCTION**  
Contractor Implements Renovations

6 **CONSTRUCTION CLOSEOUT**  
Final Inspection for Quality Assurance

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2017	Q2 2017	Q1 2018	Q3 2018	Q2 2019	Q1 2020
New Planned	Q1 2017	Q2 2017	Q1 2018	Q3 2019	Q1 2020	Q1 2021
Actual/Forecast	4/1/2017	6/22/2017	12/19/2017	4/9/2019	Q3 2020	

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$851,000
HVAC Improvements	\$672,000

**COMMENTS:**

Reason: Delays have occurred during bid and award. Funding Year 1 thru 3 projects are to take priority for advertisement of bid.  
Remedy: The project is funded under Year 4 and was advertised after the available funding Year 1 thru 3 projects were advertised.  
Bid opening has taken place and the project is pending Board

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	N/A	N/A

<b>SCOPE:</b>	<b>BUDGET:</b>
HVAC Improvements - Chiller Replacement	\$154,000

**COMMENTS:**

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Dillard Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **93% Complete**

SCHEDULE:	<div><div>PH:1 Planning/Design</div><div>PH:2 Implement</div><div>PH:3 Complete</div></div>			
	Planned	Q4 2017	Q2 2018	TBD
	Actual	11/2017	06/2018	
SCOPE:				
School Choice Enhancement				
BUDGET:				
\$100,000				
FLAG:				
<div>COMMENTS:</div> <div>Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.</div>				

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Discovery Elementary School

8800 NW 54 COURT, SUNRISE 33351

Location Num	3962
Board District	5
Board Member	Dr. Rosalind Osgood
ADEFP Budget*	\$613,000
Total Facilities Budget	\$250,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Complete

Primary Renovation: Test and Balance services is completed by a licensed contractor without standard design services. Test and Balance report submitted. The report is being reviewed by OFC prior to signoff of completion.

School Choice Enhancements: Voting completed 6/8/16. PE equipment, classroom carpets and books delivered 09/2016. Stage curtains, furniture, two portable sound systems delivered 11/2016. Cabinets, podiums, outdoor benches and tables delivered 03/2017. Tricaster delivered 06/2017. TVs delivered 12/2017. Cafeteria Sound System and projector delivered and installed 02/2018. Murals completed 12/2018. (2) golf carts delivered 01/2020. Front office furniture and fabric for chairs on order.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **10% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2018	N/A	N/A	Q4 2019	Q2 2020	Q3 2020
New Planned	Q3 2018	N/A	N/A	Q4 2019	Q2 2020	Q3 2020
Actual/Forecast	5/1/2017	N/A	N/A	5/29/2018	10/1/2018	3/27/2020
SCOPE:			BUDGET:	FLAG:		
HVAC Improvements			\$150,000	COMMENTS:		

#### School Choice Enhancements\*

Phase: **90% Complete**

SCHEDULE:		PH:1 Planning/Design		PH:2 Implement		PH:3 Complete	
Planned	Q1 2015		Q2 2016		TBD		TBD
Actual	11/2015		06/2016				
SCOPE:		BUDGET:		FLAG:			
School Choice Enhancement		\$100,000		<b>COMMENTS:</b> Pending delivery of furniture. Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.

FLAG KEY: S=Schedule B= Budget

S-Project Delayed=Schedule: Project has missed the planned milestone date for progressing to the next phase in the process.

S-Delay Possible=Schedule: Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

B=Budget: reflects a need for board approved increase in funding based on bid and/or change order results.

Page 305 -- FY20 Q3



## Dolphin Bay Elementary School

16450 MIRAMAR PARKWAY, MIRAMAR 33027

Location Num	3751
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$307,000
Total Facilities Budget	\$100,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.


- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


### PRIMARY PROJECTS CURRENT STATUS: **N/A**

School Choice Enhancements: COMPLETED 04/2019 - Voting completed 3/24/17. Projectors delivered 05/2017. Morning Announcement Studio Equipment, Recordex, Laptops delivered 8/2017. Playground upgrades, new play equipment Pre-K installed 12/2018. (1) Laptop, (8) Projectors and (1) ThinkPad delivered 04/2019.

### SMART Facilities Update By Project



#### School Choice Enhancements\*

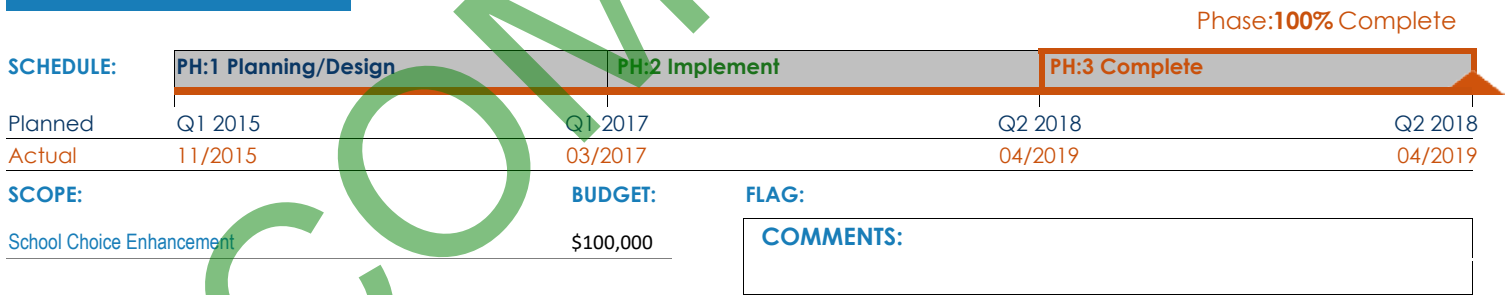

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Dr. Martin Luther King, Jr. Montessori Academy

591 NW 31 AVENUE, LAUDERHILL 33311

Location Num	1611
Board District	5
Board Member	Dr. Rosalind Osgood
ADEFP Budget*	\$1,348,615
Total Facilities Budget	\$1,161,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Complete

Primary Renovation: Project is in substantial completion. Close-out in progress.

School Choice Enhancements: COMPLETED 09/2019 - Voting completed 8/25/17. Interiors murals delivered 9/2016. Outdoor benches delivered 11/2016. Laptop computers, teachers' laptops, printers, Think Pads and Promethean boards delivered 01/2017. Marquee permit issued 12/27/2018; Marquee completed 03/2019. (1) Lenovo laptop delivered 09/2019.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: 10% Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2016	Q4 2016	Q2 2017	Q3 2017	Q2 2018	Q1 2019
New Planned	Q4 2016	Q4 2016	Q2 2017	Q3 2017	Q4 2018	Q4 2019
Actual/Forecast	11/7/2016	11/7/2016	4/10/2017	10/3/2018	11/15/2018	3/30/2020
SCOPE:			BUDGET:	FLAG:		
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)			\$86,000	COMMENTS:		
Fire Sprinklers			\$762,000			

#### HVAC Improvements

Phase: 100% Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	N/A	3/21/2018
SCOPE:			BUDGET:	FLAG:		
HVAC Improvements - Chiller Replacement			\$146,175	COMMENTS:		
HVAC Improvements - Other			\$66,825			

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Dr. Martin Luther King, Jr. Montessori Academy

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete	
Planned	Q1 2015	Q3 2016	Q1 2018	Q1 2018
Actual	11/2015	08/2016	09/2019	09/2019
SCOPE:				
School Choice Enhancement				
BUDGET:				
\$100,000				
FLAG:				
COMMENTS:				

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Driftwood Elementary School

2700 NW 69 AVENUE, HOLLYWOOD 33024

Location Num	0721
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$2,080,000
Total Facilities Budget	\$1,835,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in progress. Addendum to Professional Service Agreement for supplemental services related to additional civil scope is pending Board approval.

School Choice Enhancements: Kick-off meeting held during SAC on 1/15/2019. Ballot Development in progress.

### SMART Facilities Update By Project



#### Primary Renovation

 Phase: **88% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q1 2019	Q3 2019	Q2 2020	Q2 2020
New Planned	Q1 2018	Q2 2018	Q1 2019	Q4 2019	Q3 2020	Q2 2021
Actual/Forecast	7/1/2017	9/20/2017	5/3/2018	Q3 2020		

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,428,000
Fire Sprinklers	\$7,000
HVAC Improvements	\$300,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred during the design phase related to clarification in fire sprinkler scope of services and additional civil scope requirements. Remedy: Decision has been made on the fire sprinkler scope of work, and the civil scope of work will be added to the project pending approval of the agreement addendum.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Driftwood Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **25%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2018	TBD	TBD
Actual	11/2018		

SCOPE:	BUDGET:	FLAG:
School Choice Enhancement	\$100,000	<b>COMMENTS:</b> Planned date for Implementation phase shown as TBD will be provided after voting process has been completed by the school community.

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Driftwood Middle School

2751 NW 70 TERRACE, HOLLYWOOD 33024

Location Num	0861
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$6,129,000
Total Facilities Budget	\$5,644,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Bid opening has occurred with Board award pending April 2020.

School Choice Enhancements: COMPLETE - Voting authorized 11/28/17 - Voting completed 1/31/18. Golf Carts delivered 04/2018. Indoor furniture for the computer lab, including tables, chairs, storage cabinets, bookcases, delivered 11/2018. Athletic equipment will be delivered once the floor in the weight room is replaced. (1) Vacuum delivered 4/2019. Athletic equipment delivered 9/2019.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **35% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2016	Q3 2016	Q2 2017	Q1 2018	Q3 2018	Q4 2019
New Planned	Q3 2016	Q3 2016	Q2 2017	Q1 2019	Q3 2019	Q4 2020
Actual/Forecast	8/12/2016	9/20/2016	5/2/2017	8/7/2019	Q2 2020	Q4 2021

#### SCOPE:

Art Room Renovation and Equipment	\$85,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$2,332,000
Conversion of Existing Space to Music and/or Art Lab(s)	\$284,000
Electrical Improvements	\$675,000
Fire Sprinklers	\$18,000
HVAC Improvements	\$1,808,000
Media Center improvements	\$293,000
Safety / Security Upgrade	\$49,000

#### BUDGET:

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays occurred during the permitting process in the design phase. The design firm has needed over 100 days to complete and resubmit the construction documents for permit. Remedy: The Letter of Recommendation to Permit has been received, and the project is progressing.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Driftwood Middle School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2016	Q1 2018	Q3 2019
Actual	01/2016	01/2018	09/2019

#### SCOPE:

School Choice Enhancement

#### BUDGET:

\$100,000

#### FLAG:

#### COMMENTS:

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Eagle Point Elementary School

100 INDIAN TRACE, WESTON 33326

Location Num	3461
Board District	6
Board Member	Laurie Rich Levinson
ADEFP Budget*	\$6,813,450
Total Facilities Budget	\$6,245,450

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Board approval of additional funding and award to contractor took place in February 2020. Pending execution of the Notice to Proceed.

School Choice Enhancements: COMPLETED 01/2018 - Voting completed 1/11/16. Portable PA system delivered 12/2016. PIP rubber surfacing project completed 12/2016. Recordex ordered 8/2017, delivered 01/2018.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **80%Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2016	Q1 2016	Q3 2016	Q3 2017	Q1 2018	Q1 2019
New Planned	Q1 2016	Q1 2016	Q3 2016	Q2 2019	Q4 2019	Q1 2021
Actual/Forecast	1/6/2016	3/15/2016	9/26/2016	7/1/2019	Q2 2020	

#### SCOPE:

Additional Funding - Board Approved 2/4/20 (JJ-1)	\$1,325,450
Art Room Renovation and Equipment	\$65,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,383,000
Conversion of Existing Space to Music and/or Art Lab(s)	\$339,000
Fire Alarm	\$50,000
HVAC Improvements	\$2,847,000
Music Room Renovation	\$136,000

#### BUDGET:

**FLAG: SB - Project Delayed**

#### COMMENTS:

Reason: Minor delays have occurred during the design phase and bid and award phase. The design firm took an above average amount of submissions in order to receive a Letter of Recommendation to Permit. The project also required a roofing reality check which caused a delay. The purpose of the reality check is to identify opportunities for cost and scope efficiencies. Remedy: The Letter of Recommendation to Permit has been received and the roofing reality check has been completed. The project is delayed by two quarters. Budget: Additional funding of \$1,325,450 was approved by the Board on 2/4/2020 in conjunction with the approval to award the construction agreement for the project.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Eagle Point Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **100% Complete**

SCHEDULE:				
PH:1 Planning/Design		PH:2 Implement		PH:3 Complete
Planned	Q1 2015	Q1 2016	Q4 2017	Q4 2017
Actual	11/2015	01/2016	01/2018	01/2018
SCOPE:		BUDGET:	FLAG:	
School Choice Enhancement		\$100,000	COMMENTS:	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Eagle Ridge Elementary School

11500 WESTVIEW DRIVE, CORAL SPRINGS 33076

Location Num	3441
Board District	4
Board Member	Lori Alhadeff
ADEFP Budget*	\$3,718,383
Total Facilities Budget	\$3,406,383

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. Substantial completion is pending an AC unit installed in one electrical room, training for Fire Alarm Panel maintenance and repair, and the final Mechanical and Fire inspections.

School Choice Enhancements: COMPLETED 01/2018 - Voting completed 09/16. PIP resurfacing completed 01/2017. Morning show equipment delivered 01/2018.

### SMART Facilities Update By Project



#### Primary Renovation

 Phase: **99% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2016	Q2 2016	Q4 2016	Q3 2017	Q1 2018	Q1 2019
New Planned	Q1 2016	Q2 2016	Q4 2016	Q3 2017	Q1 2018	Q1 2019
Actual/Forecast	3/9/2016	5/17/2016	11/16/2016	11/16/2017	5/3/2018	5/30/2020

#### SCOPE:

Additional Funding - Board Approved 03/20/18 (JJ-4)

Fire Alarm

HVAC Improvements

#### BUDGET:

\$1,047,383

\$294,000

\$1,664,300

#### FLAG: S - Project Delayed

#### COMMENTS:

Original contractual date of substantial completion is 7/29/2019. Reason: Delays occurred in Design, and Bid and Award that were not regained during construction. A change order is forthcoming to provide the contractor a time extension. Delays in construction were due to fire alarm scope changes required to comply with the new fire alarm requirements. These delays were not the contractor's fault. Update: Fire Alarm Panel training is required for PPO and a decision is pending on the installation requirements of an AC unit for one electrical room.

FLAG KEY: S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.



## Eagle Ridge Elementary School

### SMART Facilities Update by Project Cont.

#### HVAC Improvements

Phase: **100%** Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout	
Planned	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	N/A	N/A	3/23/2018

<b>SCOPE:</b> HVAC Improvements - Chiller Replacement	<b>BUDGET:</b> \$300,700	<b>FLAG:</b> <b>COMMENTS:</b>
--	-----------------------------	----------------------------------

#### School Choice Enhancements\*

Phase: **100%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete	
Planned	Q1 2015	Q4 2016	Q4 2017	Q4 2017
Actual	11/2015	09/2016	01/2018	01/2018

<b>SCOPE:</b> School Choice Enhancement	<b>BUDGET:</b> \$100,000	<b>FLAG:</b> <b>COMMENTS:</b>
--	-----------------------------	----------------------------------

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Embassy Creek Elementary School

10905 SE LAKE BOULEVARD, COOPER CITY 33026

Location Num	3191
Board District	6
Board Member	Laurie Rich Levinson
ADEFP Budget*	\$5,493,700
Total Facilities Budget	\$4,964,700

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. Contractor is revising the roofing submittal in order to receive a roofing sub-permit prior to starting construction.

School Choice Enhancements: COMPLETED 07/2018 - Voting completed 5/10/17. Student laptops delivered 08/2017. Classroom projectors ceiling mounted 10/2017. Cafeteria Partitions permit received 10/2017; construction completed 02/2018. Window blinds installed 02/2018. (7) Laptops delivered 07/2018.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **1%Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2016	Q1 2017	Q4 2017	Q2 2018	Q4 2018	Q4 2019
New Planned	Q4 2016	Q1 2017	Q4 2017	Q2 2019	Q4 2019	Q4 2020
Actual/Forecast	11/18/2016	3/13/2017	8/28/2017	2/19/2019	10/29/2019	11/3/2020

#### SCOPE:

Additional Funding - Board Approved 08/06/19 (JJ-1)	\$1,340,700
Art Room Renovation and Equipment	\$65,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$770,000
Conversion of Existing Space to Music and/or Art Lab(s)	\$339,000
Fire Alarm	\$294,000
HVAC Improvements	\$1,920,000
Music Room Renovation	\$136,000

#### BUDGET:

#### FLAG:

#### COMMENTS:

Original contractual date of substantial completion is 11/3/2020. Project is currently on pace.

## Embassy Creek Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete	
Planned	Q4 2016	Q2 2017	Q2 2018	Q2 2018
Actual	12/2016	05/2017	07/2018	07/2018
SCOPE:				
School Choice Enhancement				
BUDGET:				
\$100,000				
FLAG:				
COMMENTS:				

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Endeavour Primary Learning Center

2701 NW 56 AVENUE, LAUDERHILL 33313

Location Num	3301
Board District	5
Board Member	Dr. Rosalind Osgood
ADEFP Budget*	\$2,612,790
Total Facilities Budget	\$2,460,790

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Additional funding was approved by the Board in January 2020. Pending signatures for GMP amendment prior to executing the Notice to Proceed for construction.

School Choice Enhancements:

Kick-off meeting held on 01/07/2018. Ballot received 02/2020. Ballot complies with District Standards. Voting completed 3/2020. Strike for the Main Entrance (Single Point of Entry), Video Equipment for Broadcasting Studio, and a Poster Maker, and playground upgrades (K-2) are on order.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **90% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q4 2018	Q2 2019	Q4 2019	Q2 2020
New Planned	Q1 2018	Q2 2018	Q4 2018	Q3 2019	Q4 2019	Q4 2020
Actual/Forecast	9/1/2017	11/13/2017	4/18/2018	6/3/2019	Q2 2020	

#### SCOPE:

Additional Funding - Board Approved 01/14/20 (JJ-5)	\$1,403,790
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$599,000
HVAC Improvements	\$358,000

#### BUDGET:

**FLAG: SB - Project Delayed**

#### COMMENTS:

Reason: Delays have been experienced during Bid and Award due to sub-contractor quotes and assembly of the GMP for Board approval. Remedy: Final signatures for the GMP amendment are pending. Board approval of additional funding was received. Budget: Additional funding of \$1,403,790 was approved by the Board on 1/14/2020 in conjunction with the approval to award the construction agreement for the project.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Endeavour Primary Learning Center

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **10% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q4 2018	Q1 2020	TBD	TBD
Actual	11/2018	03/2020		
<b>SCOPE:</b>	<b>BUDGET:</b>		<b>FLAG:</b>	
School Choice Enhancement	\$100,000		<b>COMMENTS:</b> Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Everglades Elementary School

2900 BONAVENTURE BOULEVARD, WESTON 33331

Location Num	2942
Board District	6
Board Member	Laurie Rich Levinson
ADEFP Budget*	\$2,941,500
Total Facilities Budget	\$2,444,500

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


## PRIMARY PROJECTS CURRENT STATUS: Construction

Primary Renovation: Construction in progress. Installation of HVAC pumps has been completed. Roofing construction is in beginning.

School Choice Enhancements: Voting completed 4/19/17. Student laptops delivered 09/2017. Scholastic Resource Room Upgrade (Media Center) delivered 11/2017. Playground upgrades cancelled due to repurposing of the funds to enhance security 5/2018.

Windscreen for the playground delivered 09/2018. Aiphone, Proximity card reader and an Aiphone sub-master installed 6/2019.

## SMART Facilities Update By Project



### Primary Renovation

Phase: 15% Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2016	Q4 2016	Q2 2017	Q4 2017	Q2 2018	Q2 2019
New Planned	Q4 2016	Q4 2016	Q2 2017	Q4 2018	Q2 2019	Q1 2020
Actual/Forecast	10/20/2016	10/20/2016	4/5/2017	11/27/2018	6/19/2019	8/31/2020

### SCOPE:

Additional Funding - Board Approved 05/07/19 (JJ-1)

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

HVAC Improvements

### BUDGET:

\$1,132,500

\$1,033,000

\$179,000

FLAG: S - Project Delayed

### COMMENTS:

Original contractual date of substantial completion is 4/14/2020. Delay Reason: Delays occurred during construction related to the roofing sub-permit process. The roofing sub-permit required multiple submissions for the sub-contractor to receive approval. The sub-permit was received in February 2020. A delay of two months was experienced in bid and award due to the roofing reality check. The roofing sub-permit process has delayed the project an additional three months with an estimated Substantial Completion date in August 2020.

FLAG KEY: S=Schedule B= Budget

S-Project Delayed=Schedule: Project has missed the planned milestone date for progressing to the next phase in the process.

S-Delay Possible=Schedule: Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

B=Budget: reflects a need for board approved increase in funding based on bid and/or change order results.

## Everglades Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **68% Complete**

SCHEDULE:		PH:1 Planning/Design		PH:2 Implement		PH:3 Complete	
Planned	Q1 2015	Q2 2017	TBD		TBD		
Actual	11/2015	04/2017					
SCOPE:		BUDGET:		FLAG:			
School Choice Enhancement		\$100,000		<div>COMMENTS:</div> <p>Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.</p>			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Everglades High School

17100 SW 48 COURT, MIRAMAR 33027

Location Num	3731
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$8,040,254
Total Facilities Budget	\$6,597,254

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. Test and Balance is in progress. Roofing and HVAC upgrades are in progress.

School Choice Enhancements: COMPLETED 03/2018 - Voting authorized 11/28/17 - Voting completed 12/19/17 - (330) laptops delivered 03/2018. (6) Printers delivered 02/2018. Aiphone and strike installation complete May 2018.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **65% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout	
Planned	Q2 2017	Q2 2017	Q1 2018	Q3 2018	Q1 2019	Q1 2020	Q2 2020
New Planned	Q2 2017	Q2 2017	Q1 2018	Q2 2019	Q3 2019	Q3 2021	Q3 2021
Actual/Forecast	4/14/2017	5/19/2017	12/4/2017	4/3/2019	8/30/2019	1/2/2021	
SCOPE:			BUDGET:		FLAG:		
Additional Funding - Board Approved 08/06/19 (JJ-3)			\$2,707,254		<div>COMMENTS:</div> <div>Original contractual date of substantial completion is 1/2/2021. Project is currently on pace.</div>		
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)			\$2,794,000				
HVAC Improvements			\$875,000				

#### Weight Room

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout		
	Planned	Q2 2017	Q2 2017	Q3 2017	Q3 2017	Q3 2017	Q4 2017	Q4 2017
	Actual/Forecast	5/5/2017	5/12/2017	7/13/2017	8/2/2017	11/12/2017	1/10/2018	1/13/2018
SCOPE:			BUDGET:		FLAG:			
Weight Room Renovation			\$121,000		COMMENTS:			

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Everglades High School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **100% Complete**

<b>SCHEDULE:</b>	<b>PH:1 Planning/Design</b>		<b>PH:2 Implement</b>	<b>PH:3 Complete</b>
Planned	Q1 2015		Q4 2017	Q1 2018
Actual	11/2015		12/2017	03/2018
<b>SCOPE:</b>	<b>BUDGET:</b>		<b>FLAG:</b>	
School Choice Enhancement	\$100,000		<b>COMMENTS:</b>	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Fairway Elementary School

7850 FAIRWAY BOULEVARD, MIRAMAR 33023

Location Num	1641
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$7,891,900
Total Facilities Budget	\$7,610,900

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


### PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. Site lighting and courtyard area sitework is complete. Stucco work for Building 75 is 95% complete. HVAC renovations in cafeteria is nearing completion. Roofing work is in progress.

School Choice Enhancements:

COMPLETED 03/2020 - Voting completed 9/2/16. Color poster maker delivered 10/2016. Two-way radios, projectors and document cameras delivered 12/2016. Morning show equipment delivered 01/2017. Sound Stage Projector delivered 11/2017. Cafeteria Sound system delivered 01/2018. Microphones for the sound system installed 02/2018. (30) laptops delivered 04/2018. Marquee completed 08/2018. (3) ThinkPads delivered 12/2018, One laptop and adaptors delivered 08/2019. TV installation completed 05/2019. (1)

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **30% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2016	Q2 2016	Q1 2017	Q4 2017	Q1 2018	Q1 2019
New Planned	Q2 2016	Q2 2016	Q1 2017	Q1 2019	Q2 2019	Q4 2020
Actual/Forecast	4/18/2016	6/15/2016	2/6/2017	1/18/2019	6/25/2019	8/14/2020

#### SCOPE:

Additional Funding - Board Approved 05/07/19 (JJ-2)	\$3,507,900
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,408,000
Electrical Improvements	\$366,000
Fire Alarm	\$294,000
HVAC Improvements	\$1,570,000
Media Center improvements	\$172,000
Safety / Security Upgrade	\$193,000

#### BUDGET:

#### FLAG:

#### COMMENTS:

Original contractual date of substantial completion is 8/14/2020. Project is currently on pace.

## Fairway Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **100% Complete**

<b>SCHEDULE:</b>	<b>PH:1 Planning/Design</b>		<b>PH:2 Implement</b>	<b>PH:3 Complete</b>
Planned	Q1 2016	Q4 2016	Q1 2020	Q1 2020
Actual	01/2016	09/2016	02/2020	02/2020
<b>SCOPE:</b>	<b>BUDGET:</b>		<b>FLAG:</b>	
School Choice Enhancement	\$100,000		<b>COMMENTS:</b>	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Falcon Cove Middle School

4251 BONAVENTURE BOULEVARD, WESTON 33332

Location Num	3622
Board District	6
Board Member	Laurie Rich Levinson
ADEFP Budget*	\$23,566,000
Total Facilities Budget	\$22,888,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction is in progress. Site drainage work and foundation work is complete. Sheer wall installation in progress.

School Choice Enhancements: COMPLETED 09/2017 - Voting completed 5/26/17. Student laptops delivered 08/2017. Recordex delivered 09/2017.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **15% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2016	Q4 2016	Q3 2017	Q4 2018	Q3 2019	Q3 2020
New Planned	Q4 2016	Q4 2016	Q3 2017	Q4 2018	Q3 2019	Q3 2020
Actual/Forecast	12/5/2016	12/20/2016	6/2/2017	6/20/2019	6/26/2019	12/30/2020

SCOPE:	BUDGET:
Additional Funding - Board Approved 06/11/19 (JJ-10)	\$12,047,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$880,000
CR Addition to allow for removal of portable buildings	\$9,546,000
HVAC Improvements	\$315,000

FLAG: **S - Delay Possible**

#### COMMENTS:

Original contractual date of substantial completion is 6/30/2020. The project has experienced delays due to as-built conditions in the field differing from the as-built plans for the campus. Additional time was needed to locate and redesign conditions for the water line and sanitary line locations below grade.

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2016	Q2 2017	Q1 2018
Actual	12/2016	05/2017	09/2017

SCOPE:	BUDGET:
School Choice Enhancement	\$100,000

FLAG:

#### COMMENTS:

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.

FLAG KEY: **S**=Schedule **B**= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

Page 327 -- FY20 Q3



## Flamingo Elementary School

1130 SW 133 AVENUE, DAVIE 33325

Location Num	2541
Board District	6
Board Member	Laurie Rich Levinson
ADEFP Budget*	\$5,188,630
Total Facilities Budget	\$2,055,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only

- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Bid opening has occurred. Pending Board approval to award.

School Choice Enhancements:

COMPLETED 03/2018 - Voting completed 11/10/2017 - Partial Replacement of sand with PIP Rubber in the playground completed 3/2018. Golf Cart delivered 12/2017. iPad and laptops delivered 01/2018.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **55% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q4 2017	Q3 2018	Q1 2019	Q4 2019
New Planned	Q2 2017	Q2 2017	Q4 2017	Q3 2019	Q4 2019	Q4 2020
Actual/Forecast	12/6/2017	12/6/2017	4/19/2018	11/13/2019	Q3 2020	Q1 2021

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

HVAC Improvements

Media Center improvements

#### BUDGET:

\$227,000

\$1,443,000

\$285,000

**FLAG: S - Project Delayed**

#### COMMENTS:

Reason: Delays have occurred in the permitting process of the design phase. The design firm has taken an above average amount of submissions in order to receive a Letter of Recommendation to Permit. Remedy: The owner will be enforcing terms of the contract for delays and multiple resubmissions. Update: The project bid opening has occurred. Pending Board approval to award.

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Flamingo Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete	
Planned	Q4 2016	Q4 2017	Q1 2018	Q1 2018
Actual	12/2016	11/2017	03/2018	03/2018
SCOPE:				
School Choice Enhancement				
BUDGET:				
\$100,000				
FLAG:				
COMMENTS:				

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.





## Floranada Elementary School

5251 NE 14 WAY, FORT LAUDERDALE 33334

Location Num	0851
Board District	3
Board Member	Heather P. Brinkworth
ADEFP Budget*	\$1,238,680
Total Facilities Budget	\$883,680

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Bid advertisement has taken place. Bid opening is scheduled for April 2020.

School Choice Enhancements: Re-voting completed 05/2017. Due to the delays in procuring the playground, Floranada decided to cancel the playground upgrades. Thirty (30) interactive projectors delivered 07/2017, and installed 08/2017. Digital Marquee submitted for permitting; revise and resubmit on 02/2020.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: 15% Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q1 2018	Q3 2018	Q1 2019	Q1 2020
New Planned	Q2 2017	Q2 2017	Q1 2018	Q3 2019	Q2 2020	Q1 2021
Actual/Forecast	4/1/2017	6/22/2017	12/22/2017	5/31/2019	Q3 2020	

#### SCOPE:

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

HVAC Improvements

#### BUDGET:

\$718,000

\$58,000

FLAG: S - Delay Possible

#### COMMENTS:

Funding Year 1 thru 3 projects are to take priority for advertisement of bid. The project is funded under Year 4 and has been advertised after the available funding Year 1 thru 3 projects were advertised.

FLAG KEY: S=Schedule B= Budget

S-Project Delayed=Schedule: Project has missed the planned milestone date for progressing to the next phase in the process.

S-Delay Possible=Schedule: Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

B=Budget: reflects a need for board approved increase in funding based on bid and/or change order results.

## Floranada Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **90% Complete**

<b>SCHEDULE:</b>	<div> <div>PH:1 Planning/Design</div> <div>PH:2 Implement</div> <div>PH:3 Complete</div> </div>			
Planned	Q1 2015	Q2 2017	Q4 2017	Q4 2017
Actual	11/2015	05/2017		

#### SCOPE:

Additional Funding - Board Approved 04/23/19 (JJ-13)  
School Choice Enhancement

#### BUDGET:

\$7,680  
\$100,000

#### FLAG: S - Project Delayed

#### COMMENTS:

Delays have occurred due to termination of the previous marquee design/manufacture. The new marquee design is permitted, and the sign is in fabrication.

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Forest Glen Middle School

6501 TURTLE RUN BOULEVARD, CORAL SPRINGS 33067

Location Num	3051
Board District	4
Board Member	Lori Alhadeff
ADEFP Budget*	\$9,790,800
Total Facilities Budget	\$9,147,800

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. Roofing demolition is in progress. Campus painting scope has begun. HVAC installation at Bldg 3 has begun.

School Choice Enhancements: COMPLETED 01/2019 - Voting completed 10/11/17 - Murals completed 12/2017. Computer Lab furniture and a TV Studio equipment delivered 03/2018. Computer lab furniture delivered 06/2018. Library Remodeling delivered 06/2018. Gym, bleachers permit issued 12/2018; bleachers installed 01/2019.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **15% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2016	Q4 2016	Q2 2017	Q1 2018	Q4 2018	Q1 2020
New Planned	Q4 2016	Q4 2016	Q2 2017	Q1 2019	Q2 2019	Q4 2020
Actual/Forecast	10/21/2016	12/6/2016	5/25/2017	1/31/2019	9/13/2019	11/22/2020

#### SCOPE:

Additional Funding - Board Approved 06/11/19 (JJ-2)

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

Fire Sprinklers

HVAC Improvements

#### BUDGET:

\$3,858,800

\$2,690,000

\$16,000

\$2,179,739

#### FLAG:

#### COMMENTS:

Original contractual date of substantial completion is 11/22/2020. Project is currently on pace.

#### HVAC Improvements

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	N/A	N/A

#### SCOPE:

HVAC Improvements - Chiller Replacement

#### BUDGET:

\$303,261

#### FLAG:

#### COMMENTS:

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Forest Glen Middle School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2016	Q4 2017	Q1 2018
Actual	12/2016	10/2017	01/2019
SCOPE:	BUDGET:		
School Choice Enhancement	\$100,000		
FLAG:			
COMMENTS:			

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



## Forest Hills Elementary School

3100 NW 85 AVENUE, CORAL SPRINGS 33065

Location Num	2631
Board District	4
Board Member	Lori Alhadeff
ADEFP Budget*	\$5,097,601
Total Facilities Budget	\$4,912,601

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction is in progress. All work completed, except the roofing renovations. The roofing permit requires multiple revisions prior to receiving the roofing sub-permit. Roofing resubmittal is pending.

School Choice Enhancements: COMPLETED - PIP rubber surfacing project completed 12/2016. Digital marquee permitted; installation completed 01/2019. Internal Cell Battery delivered 04/2019. (3) Lenovo laptops delivered 06/2019.

### SMART Facilities Update By Project



#### Primary Renovation

Phase: **25%Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2016	Q4 2016	Q2 2017	Q4 2017	Q3 2018	Q2 2019
New Planned	Q4 2016	Q4 2016	Q2 2017	Q4 2017	Q3 2018	Q2 2019
Actual/Forecast	10/20/2016	10/20/2016	4/10/2017	3/27/2018	8/1/2018	9/1/2020

#### SCOPE:

Additional Funding - Board Approved 06/26/18 (JJ-5)

Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)

Fire Sprinklers

Media Center improvements

#### BUDGET:

\$1,083,601

\$1,071,000

\$81,000

\$184,000

#### FLAG: S - Project Delayed

#### COMMENTS:

Original contractual date of substantial completion is 2/2/2019. Reason: Delays occurred during construction related to the roofing sub-permit. The project continues to be delayed until the roofing sub-permit is received. Remedy: The contractor has been put on notice twice. The contractor has hired a new roofing sub-contractor

#### HVAC Improvements

Phase: **100%Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	N/A	7/12/2017

#### SCOPE:

Replace existing AHUs with new.

#### BUDGET:

\$2,100,000

#### FLAG:

#### COMMENTS:

**FLAG KEY:** S=Schedule B= Budget

**S-Project Delayed=Schedule:** Project has missed the planned milestone date for progressing to the next phase in the process.

**S-Delay Possible=Schedule:** Reflects a possibility of the project missing the planned milestone date for progressing to next phase in the process.

**B=Budget:** reflects a need for board approved increase in funding based on bid and/or change order results.

## Forest Hills Elementary School

### SMART Facilities Update by Project Cont.

#### Fire Alarm

Phase: **94% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2016	Q4 2016	Q2 2017	Q4 2017	Q3 2018	Q2 2019
New Planned	Q4 2016	Q4 2016	Q2 2017	Q4 2017	Q3 2018	Q2 2019
Actual/Forecast	10/20/2016	10/20/2016	4/10/2017	Q3 2020		

#### SCOPE:

Fire Alarm

#### BUDGET:

\$293,000

#### FLAG: S - Project Delayed

#### COMMENTS:

Reason: Previous delays in the design phase occurred when the project was put on hold for coordination with the Primary Renovation. At this time the delays are now the requirement for additional funding to add a voice activation system to the Fire Alarm. Multiple bids have been required to receive a competitive cost for design and construction by a CSMP Fire Alarm Contractor. Remedy Update: The project is pending Board approval for additional funding prior to finishing design and having the contractor perform with the Primary Renovation.

#### School Choice Enhancements\*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	N/A	Q1 2018
Actual	11/2015	N/A	06/2019

#### SCOPE:

School Choice Enhancement

#### BUDGET:

\$100,000

#### FLAG:

#### COMMENTS:

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.
